

348
6/5/80
ELM

DR. 1270

DOE/NASA CONTRACTOR
REPORT

DOE/NASA CR-161435

SOLAR HEATING SYSTEM INSTALLED AT BLAKEDALE
PROFESSIONAL CENTER, GREENWOOD, S. C. - FINAL REPORT

Prepared by

W. E. Gilbert & Associates, Inc.
P. O. Box 519
Greenwood, S. C. 29646


Under Contract EX-76-C-01-2389

MASTER

Monitored by

National Aeronautics and Space Administration
George C. Marshall Space Flight Center, Alabama 35812

For the U. S. Department of Energy



U.S. Department of Energy



Solar Energy

DISTRIBUTION OF THIS DOCUMENT IS UNLIMITED

DISCLAIMER

This report was prepared as an account of work sponsored by an agency of the United States Government. Neither the United States Government nor any agency Thereof, nor any of their employees, makes any warranty, express or implied, or assumes any legal liability or responsibility for the accuracy, completeness, or usefulness of any information, apparatus, product, or process disclosed, or represents that its use would not infringe privately owned rights. Reference herein to any specific commercial product, process, or service by trade name, trademark, manufacturer, or otherwise does not necessarily constitute or imply its endorsement, recommendation, or favoring by the United States Government or any agency thereof. The views and opinions of authors expressed herein do not necessarily state or reflect those of the United States Government or any agency thereof.

DISCLAIMER

Portions of this document may be illegible in electronic image products. Images are produced from the best available original document.

NOTICE

This report was prepared to document work sponsored by the United States Government. Neither the United States nor its agents the United States Department of Energy, the United States National Aeronautics and Space Administration, nor any federal employees, nor any of their contractors, subcontractors or their employees, make any warranty, express or implied, or assume any legal liability or responsibility for the accuracy, completeness, or usefulness of any information, apparatus, product or process disclosed, or represent that its use would not infringe privately owned rights.

1. REPORT NO. DOE/NASA CR-161435		2. GOVERNMENT ACCESSION NO.		3. RECIPIENT'S CATALOG NO.	
4. TITLE AND SUBTITLE Solar Heating System Installed at Blakedale Professional Center, Greenwood, South Carolina - Final Report				5. REPORT DATE March 1980	
				6. PERFORMING ORGANIZATION CODE	
7. AUTHOR(S)				8. PERFORMING ORGANIZATION REPORT #	
9. PERFORMING ORGANIZATION NAME AND ADDRESS W. E. Gilbert and Associates, Inc. P. O. Box 519 Greenwood, South Carolina 29646				10. WORK UNIT NO.	
				11. CONTRACT OR GRANT NO. EX-76-C-01-2389	
12. SPONSORING AGENCY NAME AND ADDRESS National Aeronautics and Space Administration Washington, DC 20546				13. TYPE OF REPORT & PERIOD COVERED Contractor Report	
				14. SPONSORING AGENCY CODE	
15. SUPPLEMENTARY NOTES This work was done under the technical management of Mr. Valmore Fogle, Marshall Space Flight Center, Alabama.					
16. ABSTRACT <p>This document provides information on the solar heating system installed at the Blakedale Professional Center, in Greenwood, South Carolina. The information consists of site and building description, solar system description, performance evaluation, system problems and installation drawings.</p> <p>The solar system was designed to provide approximately 85 per cent of the building's heating requirements. The system was installed concurrently with building construction and heats 4,440 square feet of the building. There are 954 square feet of liquid flat-plate collectors that are roof-mounted and have a drain-down system to protect the collectors from freezing. A 5,000 gallon steel, polyurethane insulated tank buried underground provides storage. The system was fully instrumented for performance evaluation and integrated into the National Solar Data Network.</p>					
17. KEY WORDS			18. DISTRIBUTION STATEMENT UC59a Unclassified-Unlimited <i>William A. Brooksbank, Jr.</i> WILLIAM A. BROOKSBANK, JR. Mgr, Solar Energy Applications Projects		
19. SECURITY CLASSIF. (of this report) Unclassified		20. SECURITY CLASSIF. (of this page) Unclassified		21. NO. OF PAGES 33	22. PRICE NTIS


THIS PAGE
WAS INTENTIONALLY
LEFT BLANK

TABLE OF CONTENTS

<u>ITEM</u>	<u>PAGE</u>
I. Introduction	1
II. Summary	1
III. Site and Building Description	4
IV. Solar System Description	6
A. Collector Array	8
B. Storage System	10
C. Transport Fluid	10
D. Transport System	10
E. Space Heating System	11
F. System Control	11
1. Control Logic	11
2. Control Parameters	13
3. Solar Collection System	13
V. Performance Evaluation	13
VI. System Problems	16
A. Collector Breakage	16
B. Dropping Storage Tank Temperatures	17
C. Controls	18
VII. Appendix	
Installation Drawings	19

DISCLAIMER

This book was prepared as an account of work sponsored by an agency of the United States Government. Neither the United States Government nor any agency thereof, nor any of their employees, makes any warranty, express or implied, or assumes any legal liability or responsibility for the accuracy, completeness, or usefulness of any information, apparatus, product, or process disclosed, or represents that its use would not infringe privately owned rights. Reference herein to any specific commercial product, process, or service by trade name, trademark, manufacturer, or otherwise, does not necessarily constitute or imply its endorsement, recommendation, or favoring by the United States Government or any agency thereof. The views and opinions of authors expressed herein do not necessarily state or reflect those of the United States Government or any agency thereof.

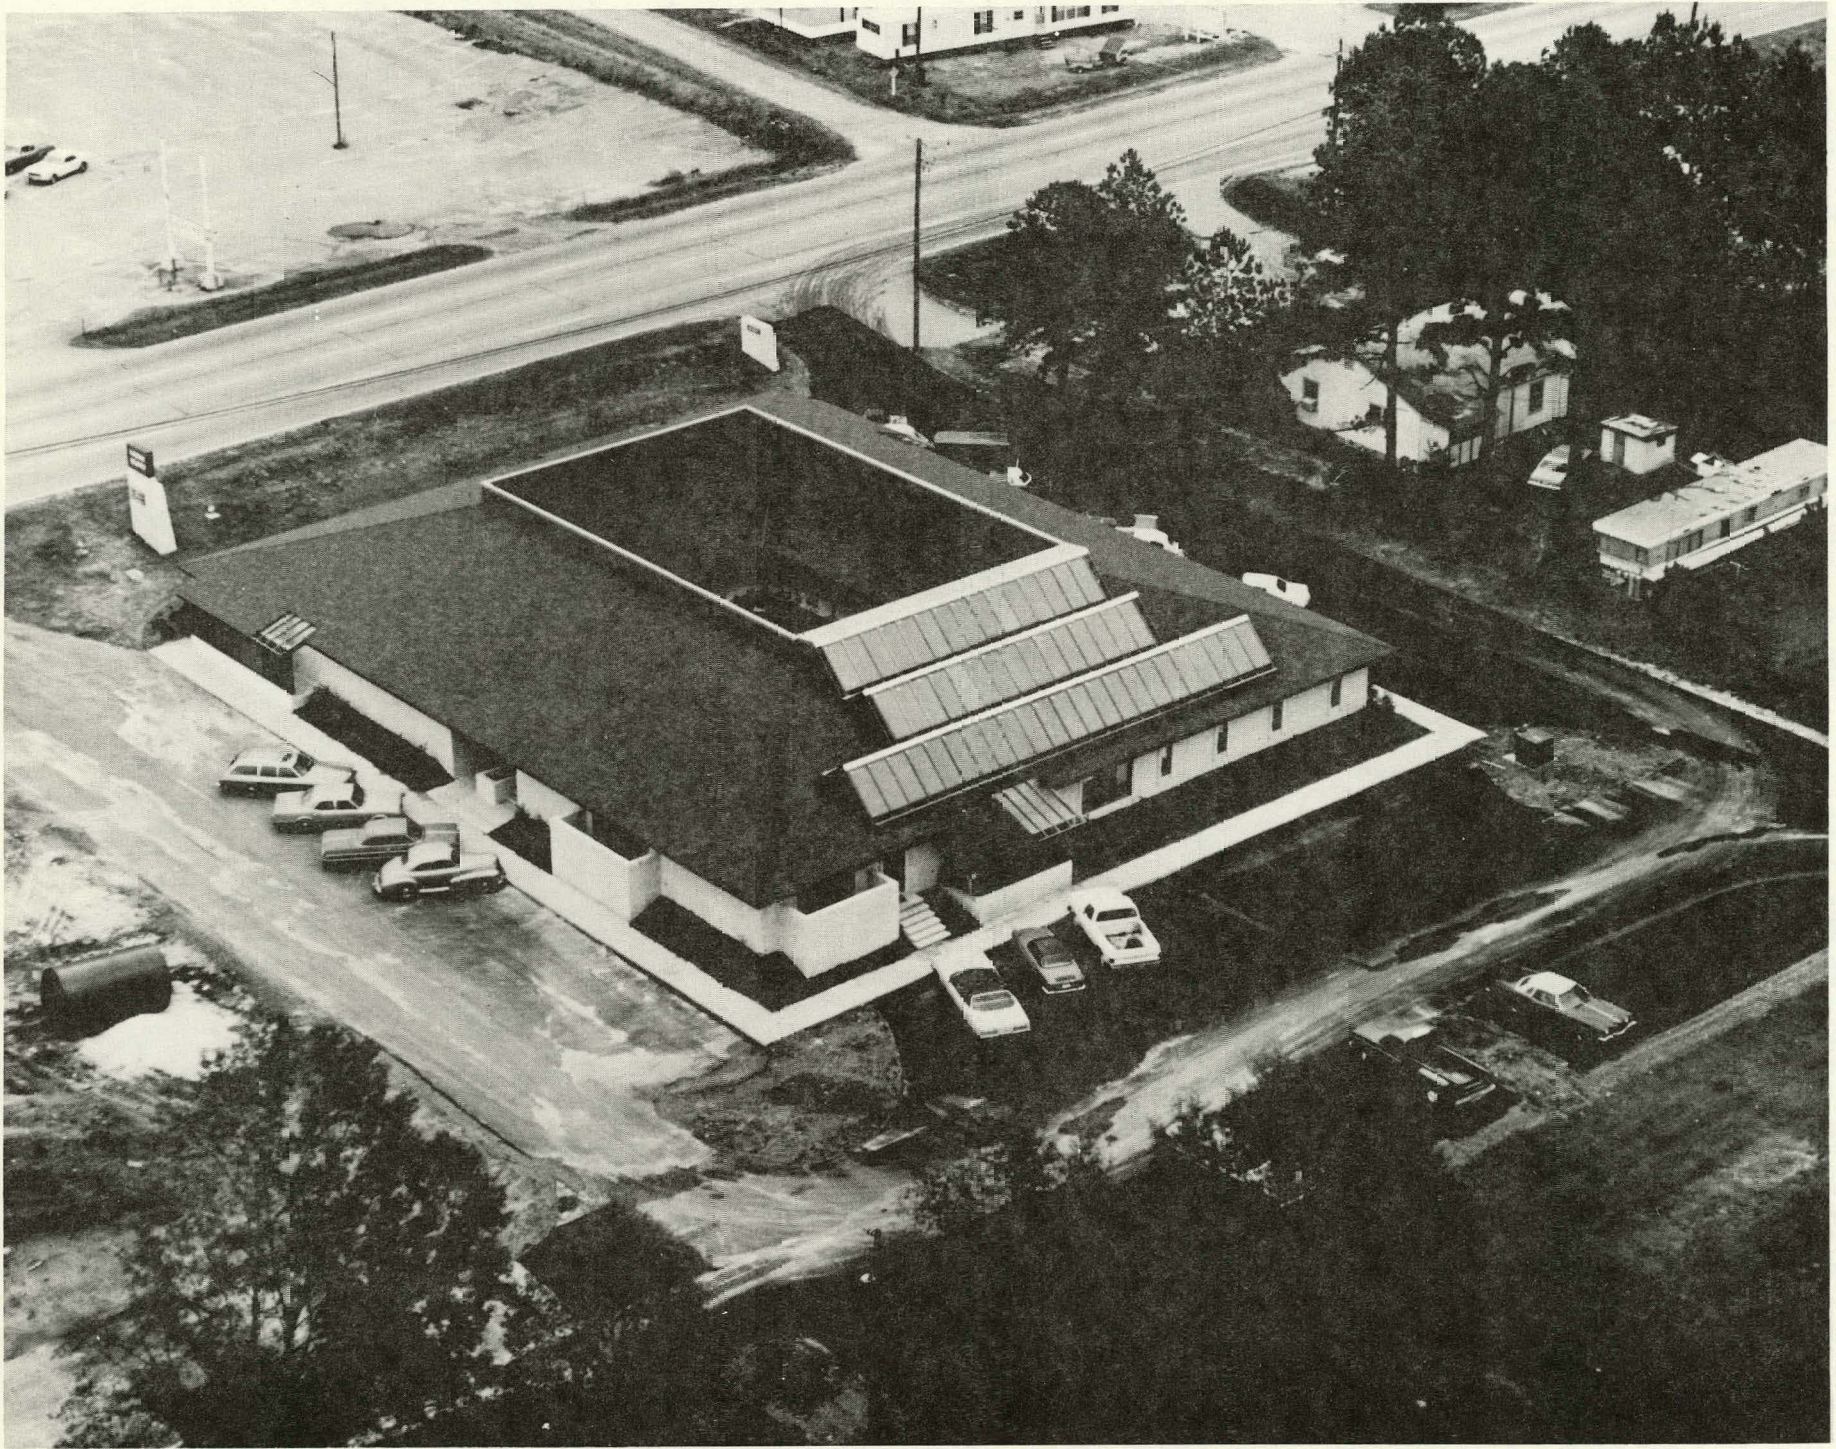

BLAKEDALE PROFESSIONAL CENTER - SOLAR COLLECTORS ON ROOF

I. INTRODUCTION

W. E. Gilbert and Associates, Inc., architects and engineers, started planning a new office complex for a client, Blakedale Professional Center, Inc., in the fall of 1974 with the idea in mind that WEG/A would be one of the building tenants and that the office suite occupied by the firm would be designed so that it would readily accept the addition of a hydronic solar heating system. In early March, 1975, the decision was made to proceed with construction of the solar system and subsequently apply for a then upcoming ERDA Program Opportunity Grant as had been outlined in the Solar Demonstration Act approved by Congress. The construction of the solar system is one hundred (100%) percent complete and the building has been occupied since September, 1975.

II. SUMMARY

The following is a brief summary of the Blakedale Professional Center solar installation. Major features of this system include:

COLLECTOR: Liquid, Flat Plate
FREEZE PROTECTION: Drain-down
APPLICATION: Heating, Hot Water
STORAGE: Liquid, Exterior, Buried
NEW/RETROFIT: New
PERFORMANCE EVALUATION INSTRUMENTATION: Yes
SITE-SPECIFIC FEATURES: Reflectors, Heat Pump

Space heating and domestic hot water heating is provided by a solar energy system utilizing 954 square feet of liquid flat plate collectors for a 10,000 square foot, one-story office building, Blakedale Professional Center, in Greenwood, South Carolina. The system was installed concurrent with building construction and heats 4,440 square feet of the building.

The collectors are roof-mounted in three banks on wooden, saw-tooth type supports with aluminized mylar reflectors on the back of the supports. The collectors are double-glazed with tempered glass and have copper absorber plates and a non-selective black coating. A drain down system protects the collectors from freezing.

A 5,000-gallon steel storage tank, covered with polyurethane insulation, is buried underground approximately 50 feet from the building.

The heat from the tank is transferred to the space through a coil in the warm air duct. A heat pump is operated downstream of the solar heating coil in the duct to provide auxiliary heat. An electric resistance coil in the duct is also furnished for additional heat when required. Service hot water is heated by a single-wall tube bundle heat exchanger immersed in the storage tank and is backed up by a 40-gallon electric water heater.

No heat exchangers are utilized between the collector, the storage tank and the solar heating coil in the duct. The piping for the system is galvanized steel and the collector fluid is treated with corrosion inhibitor.

The system has been fully instrumented for performance evaluation and integrated into the National Solar Data Network. It has been operational intermittently since August 1977.

NOTE: The original design employed collectors having aluminum absorber plated and freeze protection was provided by means of a nitrogen displacement system. These original units were replaced during 1977 with copper collectors because of glazing fractures and the nitrogen system was replaced with an atmospheric drain-down.

III. SITE AND BUILDING DESCRIPTION

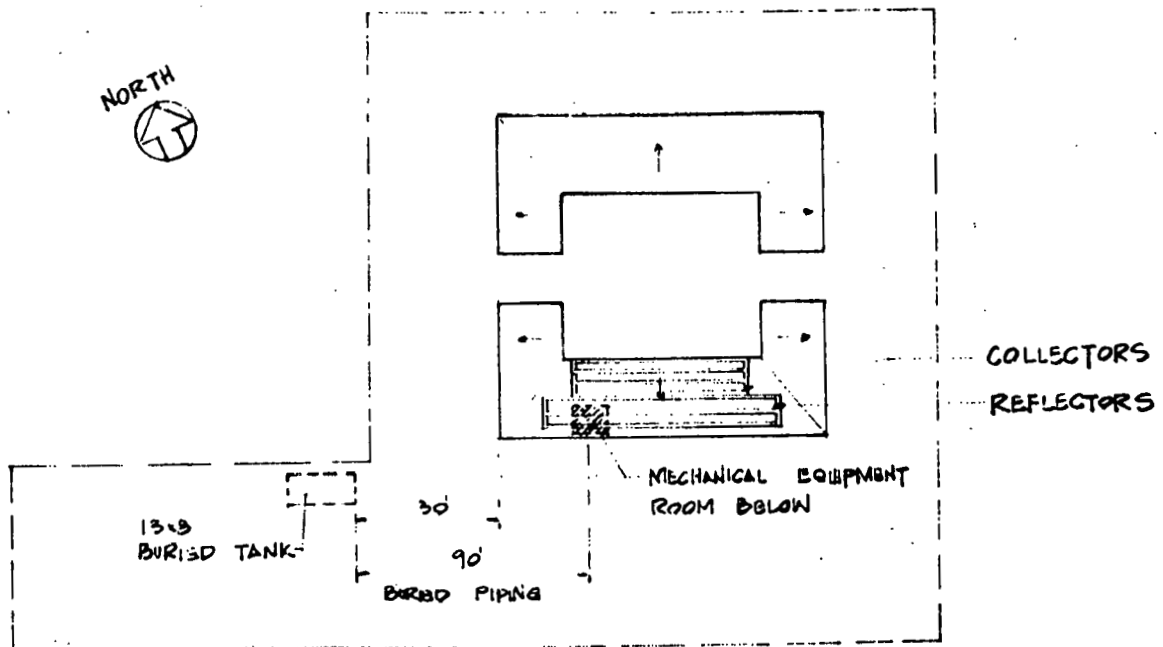


Figure III-1
Site Plan

III SITE AND BUILDING DESCRIPTION

Site Description:

- * Special topographic or climatic considerations - None
- * Latitude - 34°N
- * Annual degree days (65°F base)
 - o Heating - 2621
 - o Cooling - 1775
 - o Data Location - Columbia, South Carolina
 - o Data Reference - "Local Climatological Data Annual Summaries for 1976," Department of Commerce, National Oceanic and Atmospheric Administration

- * Average horizontal insolation
 - o January - 932 BTU/FT²-Day
 - o July - 1926 BTU/FT²-Day
 - o Data Location - Charleston, South Carolina
 - o Data Reference - Solar Heating Design by the F-Chart Method, Beckman, Klein, Duffie, Wiley-Interscience Publication, 1977

- * Site Topographic Description - Flat

- * Shading - None

Building Description:

- * Occupancy - Professional offices
- * Total area - Approximately 9552 FT.²

- * Solar conditioned area - 4284 Ft²
- * Height - Single story
- * Roof slope - Pitched, 4 in 12
- * Special features - Open inner court, 3 ft. overhang around exterior, 10 ft. overhang at courtyard

Structure:

- * Walls (Solar conditioned space)
 - o Frame - 2 X 4 wood stud
 - o Exterior finish - Stucco on metal lath on gypsum board sheathing
 - o Insulation - R-11, 3-1/2 in fiberglass batt
 - o Interior finish - Gypsum board
 - o Windows - Fixed and sliding doors, double glazed
 - o Doors - Weather stripped, no vestibule
- * Roof (Solar conditioned space)
 - o Frame - Pitched wood truss
 - o Insulation - Suspended 6 in fiberglass batts at ceiling, R-26
 - o Exterior finish - Asphalt shingles on 1/2 in plywood sheathing
 - o Floor - Concrete slab on grade

Mechanical System:

- * Heating
 - o Solar - Duct coil heat exchanger

- o Auxiliary - Air-to-air heat pump and electric resistance heating elements
- o Distribution - Duct System
- * Cooling (Non-solar)
 - o Auxiliary - Air-to-Air heat pump
 - o Distribution - Duct System
- * Domestic Hot Water
 - o Deleted From Project

IV. SOLAR SYSTEM DESCRIPTION

General: Figure IV-1 - Overall System Schematic.

Approximately eighty-five percent (85%) of the building's heating requirements are provided by an hydronic solar system. The system uses roof mounted recirculating water copper solar collection panels in conjunction with an underground hot water storage tank and recirculating pumps, piping, hot water coils and necessary instrumentation to automatically heat the system's hot water by radiated heat from the sun, and transfer this heat via the hot water coil to a conventional forced hot air ducted heating system for distribution to the office complex. The hot water system is closed and has the capability of being pressurized by nitrogen. Domestic city water mixed with one percent (1%) by volume of corrosion inhibitor is utilized as the heat transfer medium. The same inhibited water that is recirculated through solar collection panels by the solar water pump is recirculated by the coil pump through an air heating hot water coil located in the duct system. There are no heat exchangers

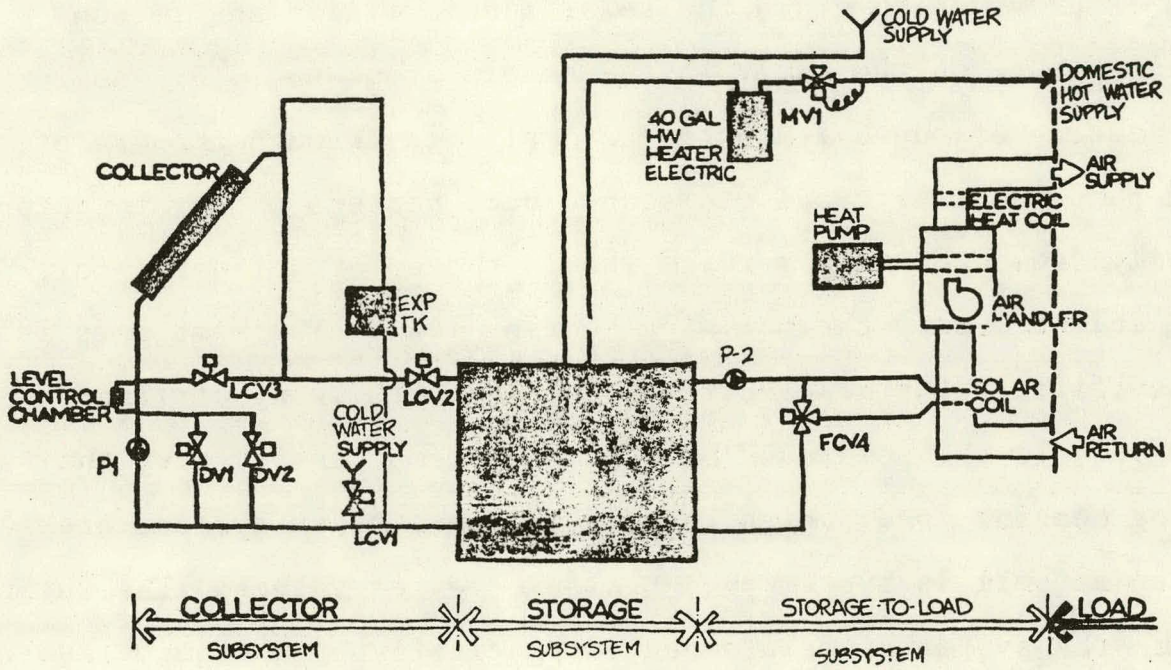


Figure IV -1
Overall System Schematic

between the solar hot water and the coil hot water. Freeze prevention of solar panels is accomplished by instrumentation which automatically drains the solar collectors anytime the temperature of the water in the storage tank is greater than the temperature of the water in the solar panels. A freeze protection back-up system is provided to drain the solar panels if for any reason the temperature of the water in the panels drops to 36°F. Auxiliary heating of the building is accomplished through the use of a heat pump and electrical resistance duct heaters which are automatically sequenced into service should the solar hot water coil not be able to carry the building heating load. The heat pump is utilized first with the electrical duct heaters being utilized in stages only if the solar and heat pump systems cannot carry the building heating load. High and low pressure alarm systems are provided as well as system over pressure relief valves. The water level in the system is maintained automatically by a liquid level control system. The roof mounted solar panel system is designed such that solar concentration on the panels is accomplished through the use of an aluminized mylar film which reflects additional sun rays onto the panels and increases the efficiency.

A. COLLECTOR ARRAY

See Figure IV-2 - Collectors, Piping and System Components & SDAS Sensors. Fifty-three (53) flat plate collectors are mounted at 45 degree tilt angle in a redwood frame superstructure on the south roof of the building. The three banks of collectors form a saw-tooth

pattern, and reflective mylar is mounted on the perpendicular face of each bank. Collector type is PPG, type I copper collectors with tempered double glazing. All collectors are fed by and discharged to insulated external headers constructed of schedule 40 galvanized carbon steel. High temperature, silicone rubber hose connects each collector to the headers, allowing for expansion and contraction.

B. STORAGE SYSTEM

A five thousand (5000) gallon steel tank 13'-6" long by 8'-0" in diameter is located underground adjacent to the building. The tank is constructed of 1/4 inch thick carbon steel plate with a rated operating pressure of 25 PSIG and temperature of 268°F, and a bursting pressure of 100 PSIG. The tank is insulated with four (4") inches of "Foamglas", having a heat transfer coefficient of 0.085 Btu/Hr-Ft²F.

C. TRANSPORT FLUID

The transport fluid is potable, municipal water with a one percent (1%) by volume concentration of corrosion inhibitor. Corrosion inhibitor is "Drewgard 100" as manufactured by the Drew Chemical Corporation.

D. TRANSPORT SYSTEM

There are essentially two separate transport systems, the energy collection system and the energy utilization system. Both systems contain in-line centrifugal pumps and schedule 40 galvanized steel piping. All parts, including valves, strainers, fittings, etc., are "off the shelf" and commercially available. Normal maintenance in accordance with manufacturers' recommendations is followed.

E. SPACE HEATING SYSTEM

The primary source of space heat is from a two (2) row, fin-tube hot water coil located in the return duct. Auxiliary energy required for the system is provided first by a ten (10) ton heat pump and, if further energy is required, by 36 KW electrical resistance duct heaters utilized in stages to satisfy the room thermostat.

F. SYSTEM CONTROL

1. Control Logic

Control of the solar pump and drain is by an electronic sensor located on the center collector in the center array. The sensor is amplified and compared with an electronic sensor located in the solar water sump, near the bottom. When the temperature of the collector is 20°F greater than the sump water temperature, the control energizes the solar pump and closes the drain valves. When the solar water sump temperature is 3°F less than the temperature

in the collectors, the pump will stop and the drain valve opens to empty the collectors. In addition, a remote bulb thermostat located at the lowest point on the collector on the roof will stop the solar pump and open the drain valve when the water temperature reaches 36°F to drain collectors to prevent freezing. Also, when the solar pump is energized, a solenoid valve will be closed by a control timer allowing both the collector panel supply and return water lines to fill up at the same time forcing the nitrogen in the lines through each of the water-air vent valves located above each bank of collectors. The control timer will then allow the normal recirculation of the collector water.

The air handling unit is programmed with a spring wound seven (7) day clock. When in the night cycle, a concealed adjustment night thermostat cycles the fan, and when the temperature falls below its setting, a timed over-ride switch returns to the day cycle.

For day cooling, the day thermostat cycles the unit fan and the cooling cycle of the heat pump upon demand. For day heating, the day thermostat cycles the unit fan and heating interlock relay. When the unit is calling for heat, the averaging bulb sensor in the unit discharge modulates the hot water 3-way valve to maintain 110°F. If the valve is fully open and the temperature is below 100°F., the heating cycle of the heat pump and electric duct heater in two stages are added in sequence through a sequencer to maintain the 100°F discharge temperature.

2. Control Parameters

The day thermostat setting for space is 75°F. This room thermostat acting through the sequencer maintains a minimum supply air temperature of 100°F on the heating mode. The night thermostat acting through a time clock maintains a room temperature of 65°F once again utilizing 100°F supply air. The hot water coil three-way valve modulates the flow of pump up to a maximum of 20 CPM at which time the sequencer utilizes the heat pump and electrical heat in stages to satisfy the room thermostat setting.

3. Solar Collection System

To prevent cycling of the solar pump on and off, an electronic sensor will not cycle the solar pump until the temperature of the solar panels is 20°F higher than the temperature of the water in the storage tank. This generally occurs around 9:00 a.m. The pump will then run, pumping .37 GPM per collector or a total of 20 GPM through fifty-three (53) collector panels until the collector temperature. At that time the pump will stop, causing a drain valve to open and drain the collectors and outside piping. The draining water displaces the nitrogen in the tank which fills the emptying collector with the inert gas.

V. PERFORMANCE EVALUATION

The National Program for Solar Heating & Cooling is being conducted

by the Department of Energy under the Solar Heating and Cooling Demonstration Act of 1974. The overall goal of this activity is to accelerate the establishment of a viable solar energy industry and to stimulate its growth in order to achieve a substantial reduction in non-renewable energy resource consumption through widespread applications of solar heating and cooling technology.

Information gathered through the Demonstration Program is disseminated in a series of site-specific reports. These reports are issued as appropriate and may include such topics as:

- Solar Project Description
- Design/Construction Report
- Project Costs
- Maintenance and Reliability
- Operational Experience
- Monthly Performance
- System Performance Evaluation

The International Business Machines Corporation is contributing to the overall goal of the Demonstration Act by monitoring, analyzing, and reporting the thermal performance of solar energy systems through analysis of measurements obtained by the National Solar Data Program.

The System Performance Evaluation Report is a product of the National Solar Data Program. Reports are issued periodically to document the

results of analysis of specific solar energy system operational performance. This report includes system description, operational characteristics and capabilities, and an evaluation of actual versus expected performance. The Monthly Performance Report, is published on a regular basis. Each parameter presented in these reports as characteristics of system performance represents over 8,000 discrete measurements obtained each month by the National Solar Data Network.

These reports issued by the National Solar Data Program for Blakedale Professional Center solar energy system are listed below and can be obtained from the Department of Energy, Technical Information Center, P.O. Box 62, Oak Ridge, Tennessee 37830.

Solar Project Description - Solar/2014-78/50

Solar Energy System Performance Evaluation - Solar/2014-79/14

Monthly Performance Reports (Select Months) - Solar/2014-78/12

Solar Project Cost Report - Solar/2014-79/60.

VI. SYSTEM PROBLEMS

As would be expected with the application of any new technology, several problems have surfaced to date. Without exception, all have been technical in nature. A brief discussion of the major problems encountered are contained herein.

A. Collector Breakage

Probably the most frustrating and costly problem was with the original aluminum flat plate collectors. In July, 1976, after the collectors had been mounted in the redwood frames and secured, five collectors incurred broken glazing. A call to PPG resulted in a prompt site visit by the sales representative, followed by months of negotiations. What was thought to be a satisfactory resolution occurred in March, 1977, when all fifty-three (53) aluminum collectors were replaced with new copper collectors at the manufacturer's expense. However, during reinstallation, several problems surfaced. Inlet and outlet connections had been relocated and re-sized, necessitating an expenditure for new silicone rubber tubing and manifold modifications, and modifications in the edge support framing. In addition, the manufacturer recommended that 3/8 inch diameter weep holes be installed in each horizontal wooden member

to allow for draining the bottom edge of each collector and prevent puddling. This recommendation apparently arose from the problem of moisture penetration of the collectors. An additional problem noted with the aluminum collectors was peeling of the flat black absorber paint.

B. DROPPING STORAGE TANK TEMPERATURE

It was noted that the storage tank temperature was dropping 5 to 10 degrees per night. It was thought that a high subsurface water table was transferring heat to the ground water, since the tank had not been completely insulated. It was later found that a malfunctioning thermo-coupler was allowing the collector recirculation pump to run continuously, thereby rejecting heat to the atmosphere at night and on cloudy days. The thermo-coupler was repaired by the instrumentation manufacturer, Barber-Coleman, and the system was placed back in service less than a month later. However, the same thermo-coupler failed again, shutting down the system. It was found that the thermo-couplers initially installed could not function continuously at temperatures of 275°F, and they were subsequently replaced.

In addition to the malfunctioning equipment, it was also substantiated that the ground water did result in heat loss from the tank. The tank was removed, completely insulated with four inches of Foamglas, and #4 washed stone was added beneath and around the

tank. No further problems of this nature have occurred.

POTABLE HOT WATER



This part of project has been deleted due to small hot water requirement and cost associated with recirculating water for so small a load.

C. CONTROLS


Far and away the biggest problems have been with controls. The design utilized 1975 off the shelf controls normally used in building hydronic systems since there was no "solar control industry" in 1975. The differential thermostats, temperature sensors and associated relays and control components have all failed at one time or another and keep the system from running for any length of time. The Owner is planning a complete control revamp program with the U.S. Department of Energy at the time of this report and should have the system ready by Fall of 1980.

VII. APPENDIX


INSTALLATION DRAWINGS

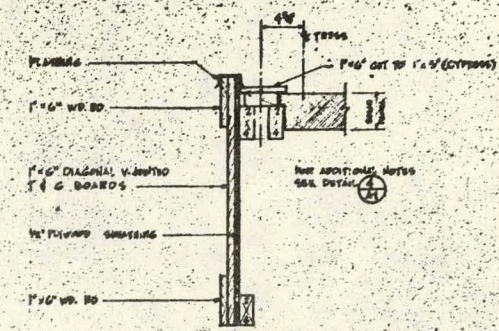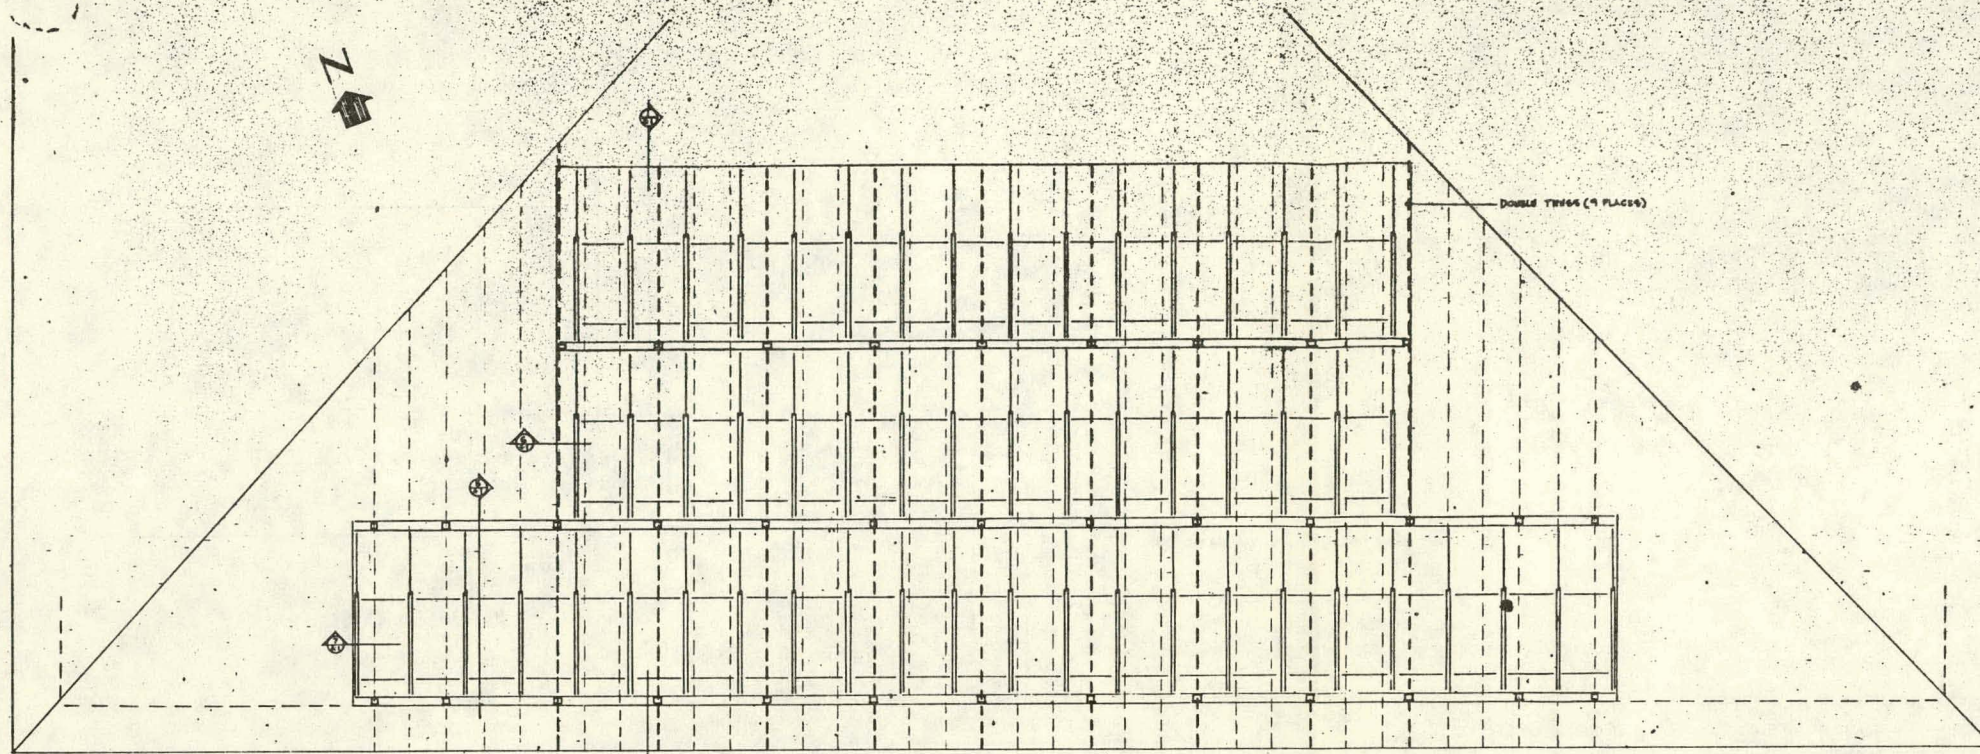


SECTION 6
1/8" = 1'-0"

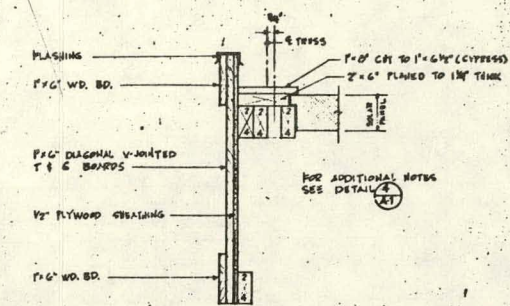


SECTION 7
1/8" = 1'-0"

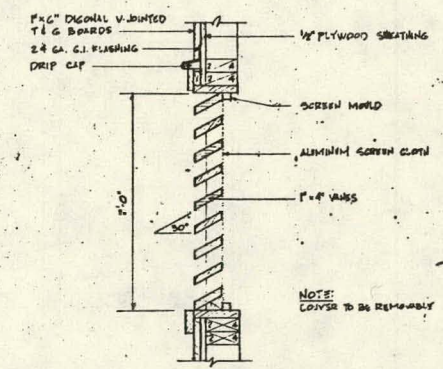


SECTION 8
1/8" = 1'-0"

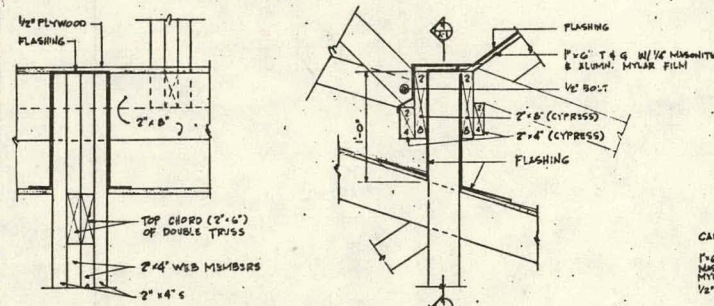


SECTION 9
1/8" = 1'-0"

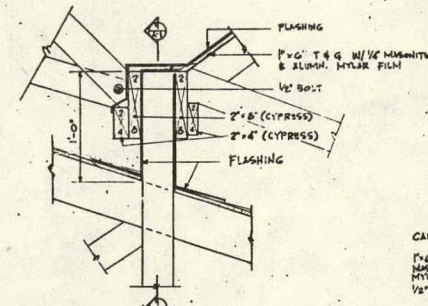


DETAIL 2
1/8" = 1'-0"

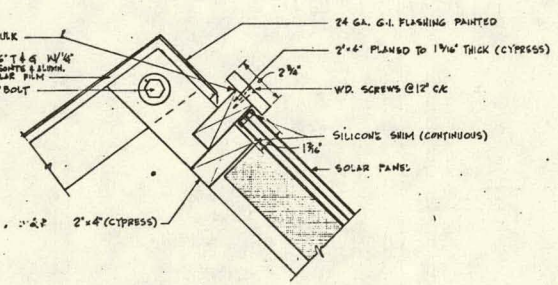


DETAIL 3
3/8" = 1'-0"

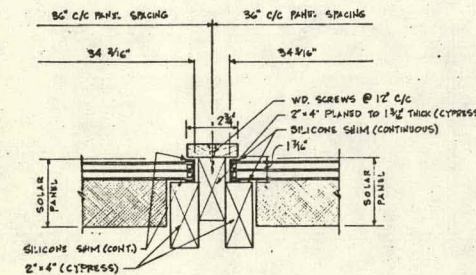


DETAIL 4
3/8" = 1'-0"

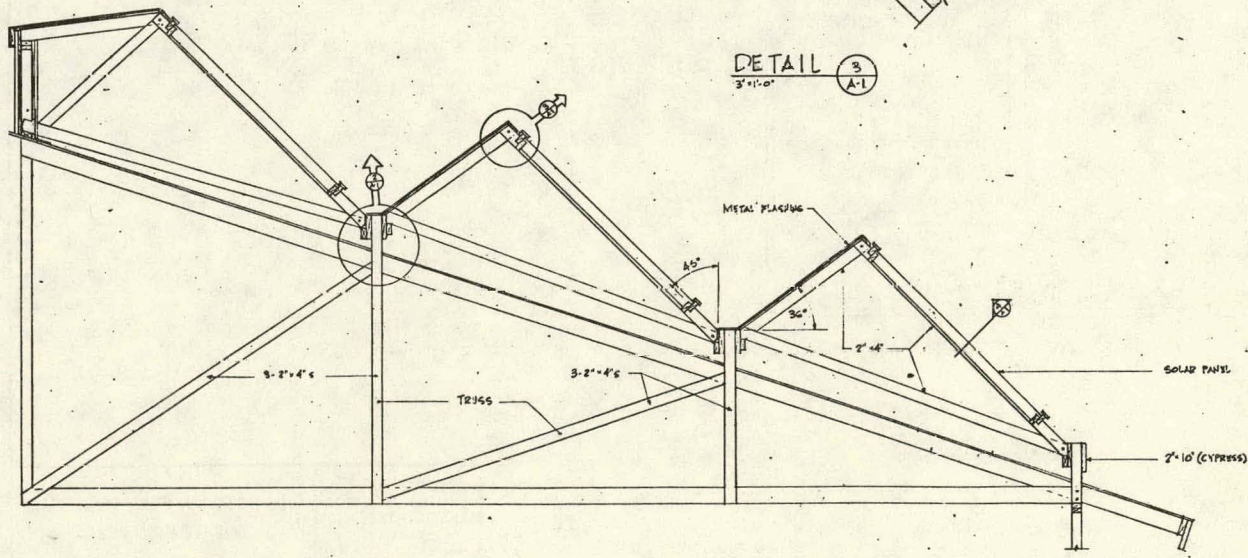

SECTION 1
1/8" = 1'-0"

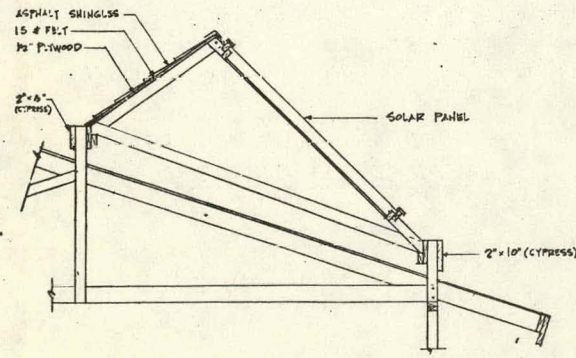


SECTION 5
1/8" = 1'-0"




KEY PLAN


W. E. GILBERT & ASSOCIATES, INC. ENGINEERS <small>GREENWOOD SOUTH CAROLINA WELCH ROAD SOUTH CAROLINA</small>		BLAKEDALE PROFESSIONAL CENTER INC. <small>SUITE No. 3</small>	
FRAMING PLAN, SECTIONS & DETAILS SOLAR PANEL SUPPORT FRAME			
DESIGNED R.W.	DATE NOV. 75	SHEET	
DRAWN L.W.	SCALE AS SHOWN	A-1	
CHECKED T.W.	FILE NO. 5-7		

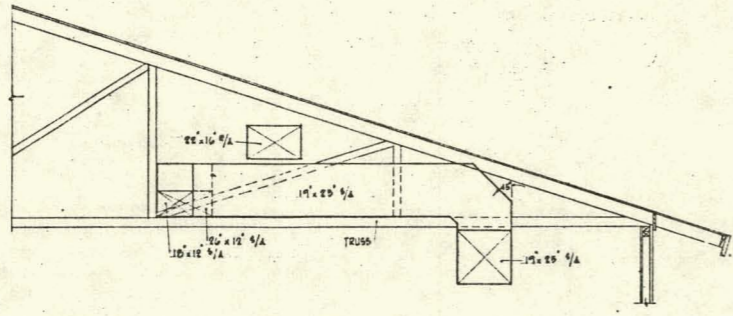


SECTION 1
SCALE 3/8" = 1'-0"

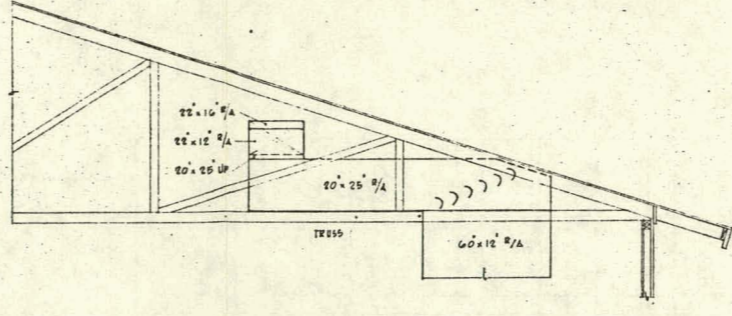


SECTION 2
SCALE 3/8" = 1'-0"

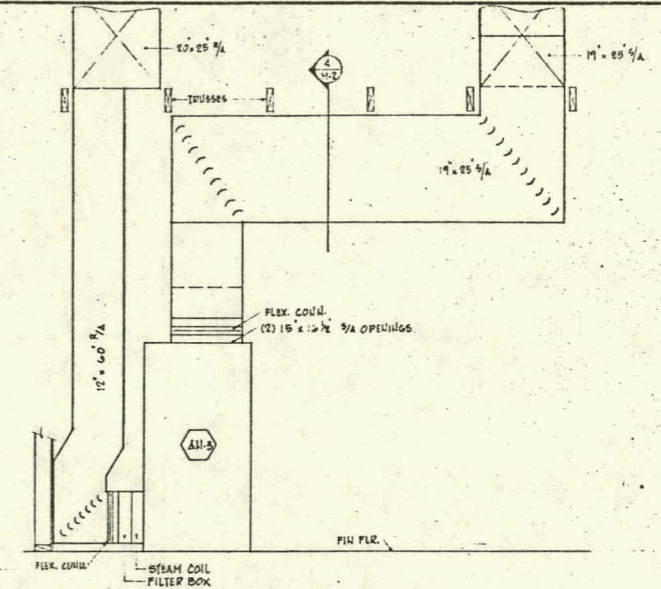

SECTION 3
SCALE 3/4" = 1'-0"

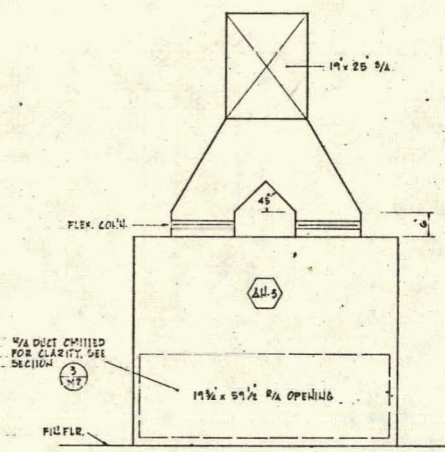


SECTION 4
SCALE 3/4" = 1'-0"

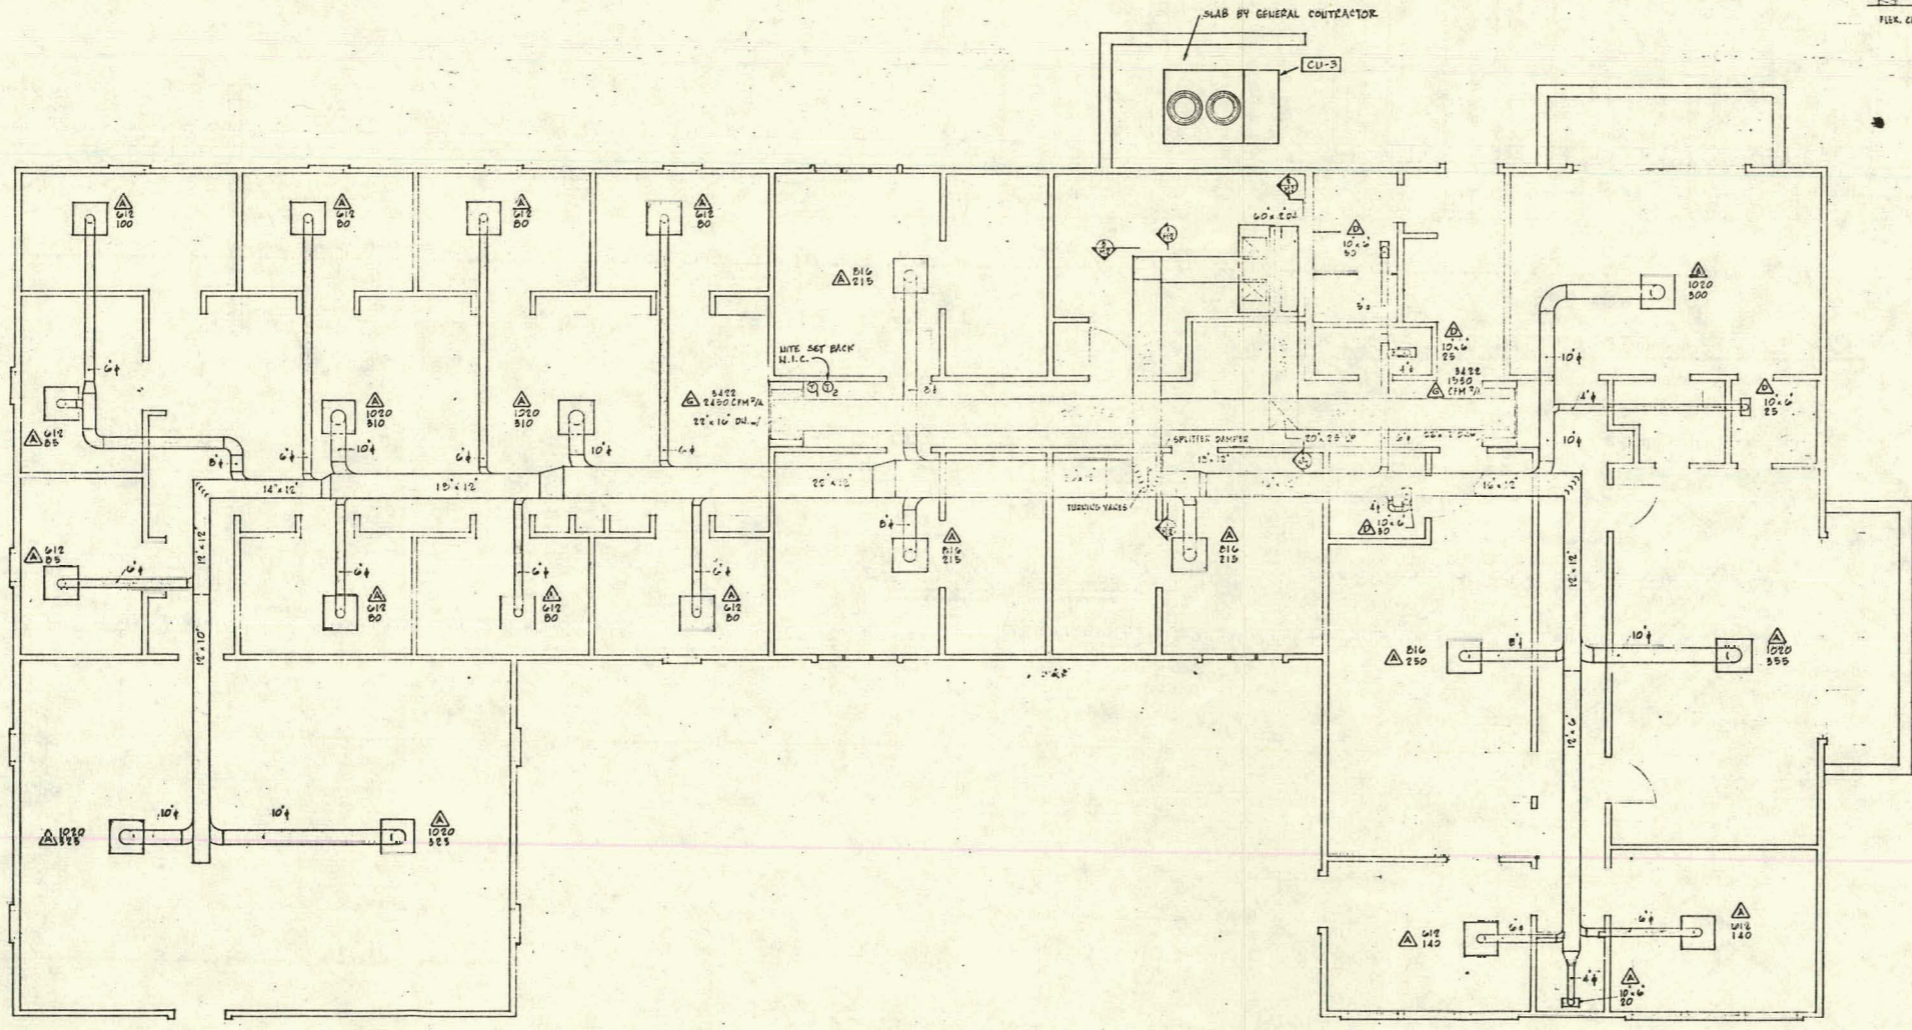

H.V.A.C. PLAN - UNIT 3
SCALE 1/4" = 1'-0"

W. E. GILBERT & ASSOCIATES, INC. ENGINEERS <small>GREENWOOD SOUTH CAROLINA HILTON HEAD SOUTH CAROLINA</small>		BLAKEDALE PROFESSIONAL CENTER INC. UNIT 3 H.V.A.C. SYSTEM	
DESIGNED A.S.S. DRAWN J.M.L. CHECKED A.S.S.	DATE SCALE AS SHOWN FILE NO. 960	SHEET M-2	21

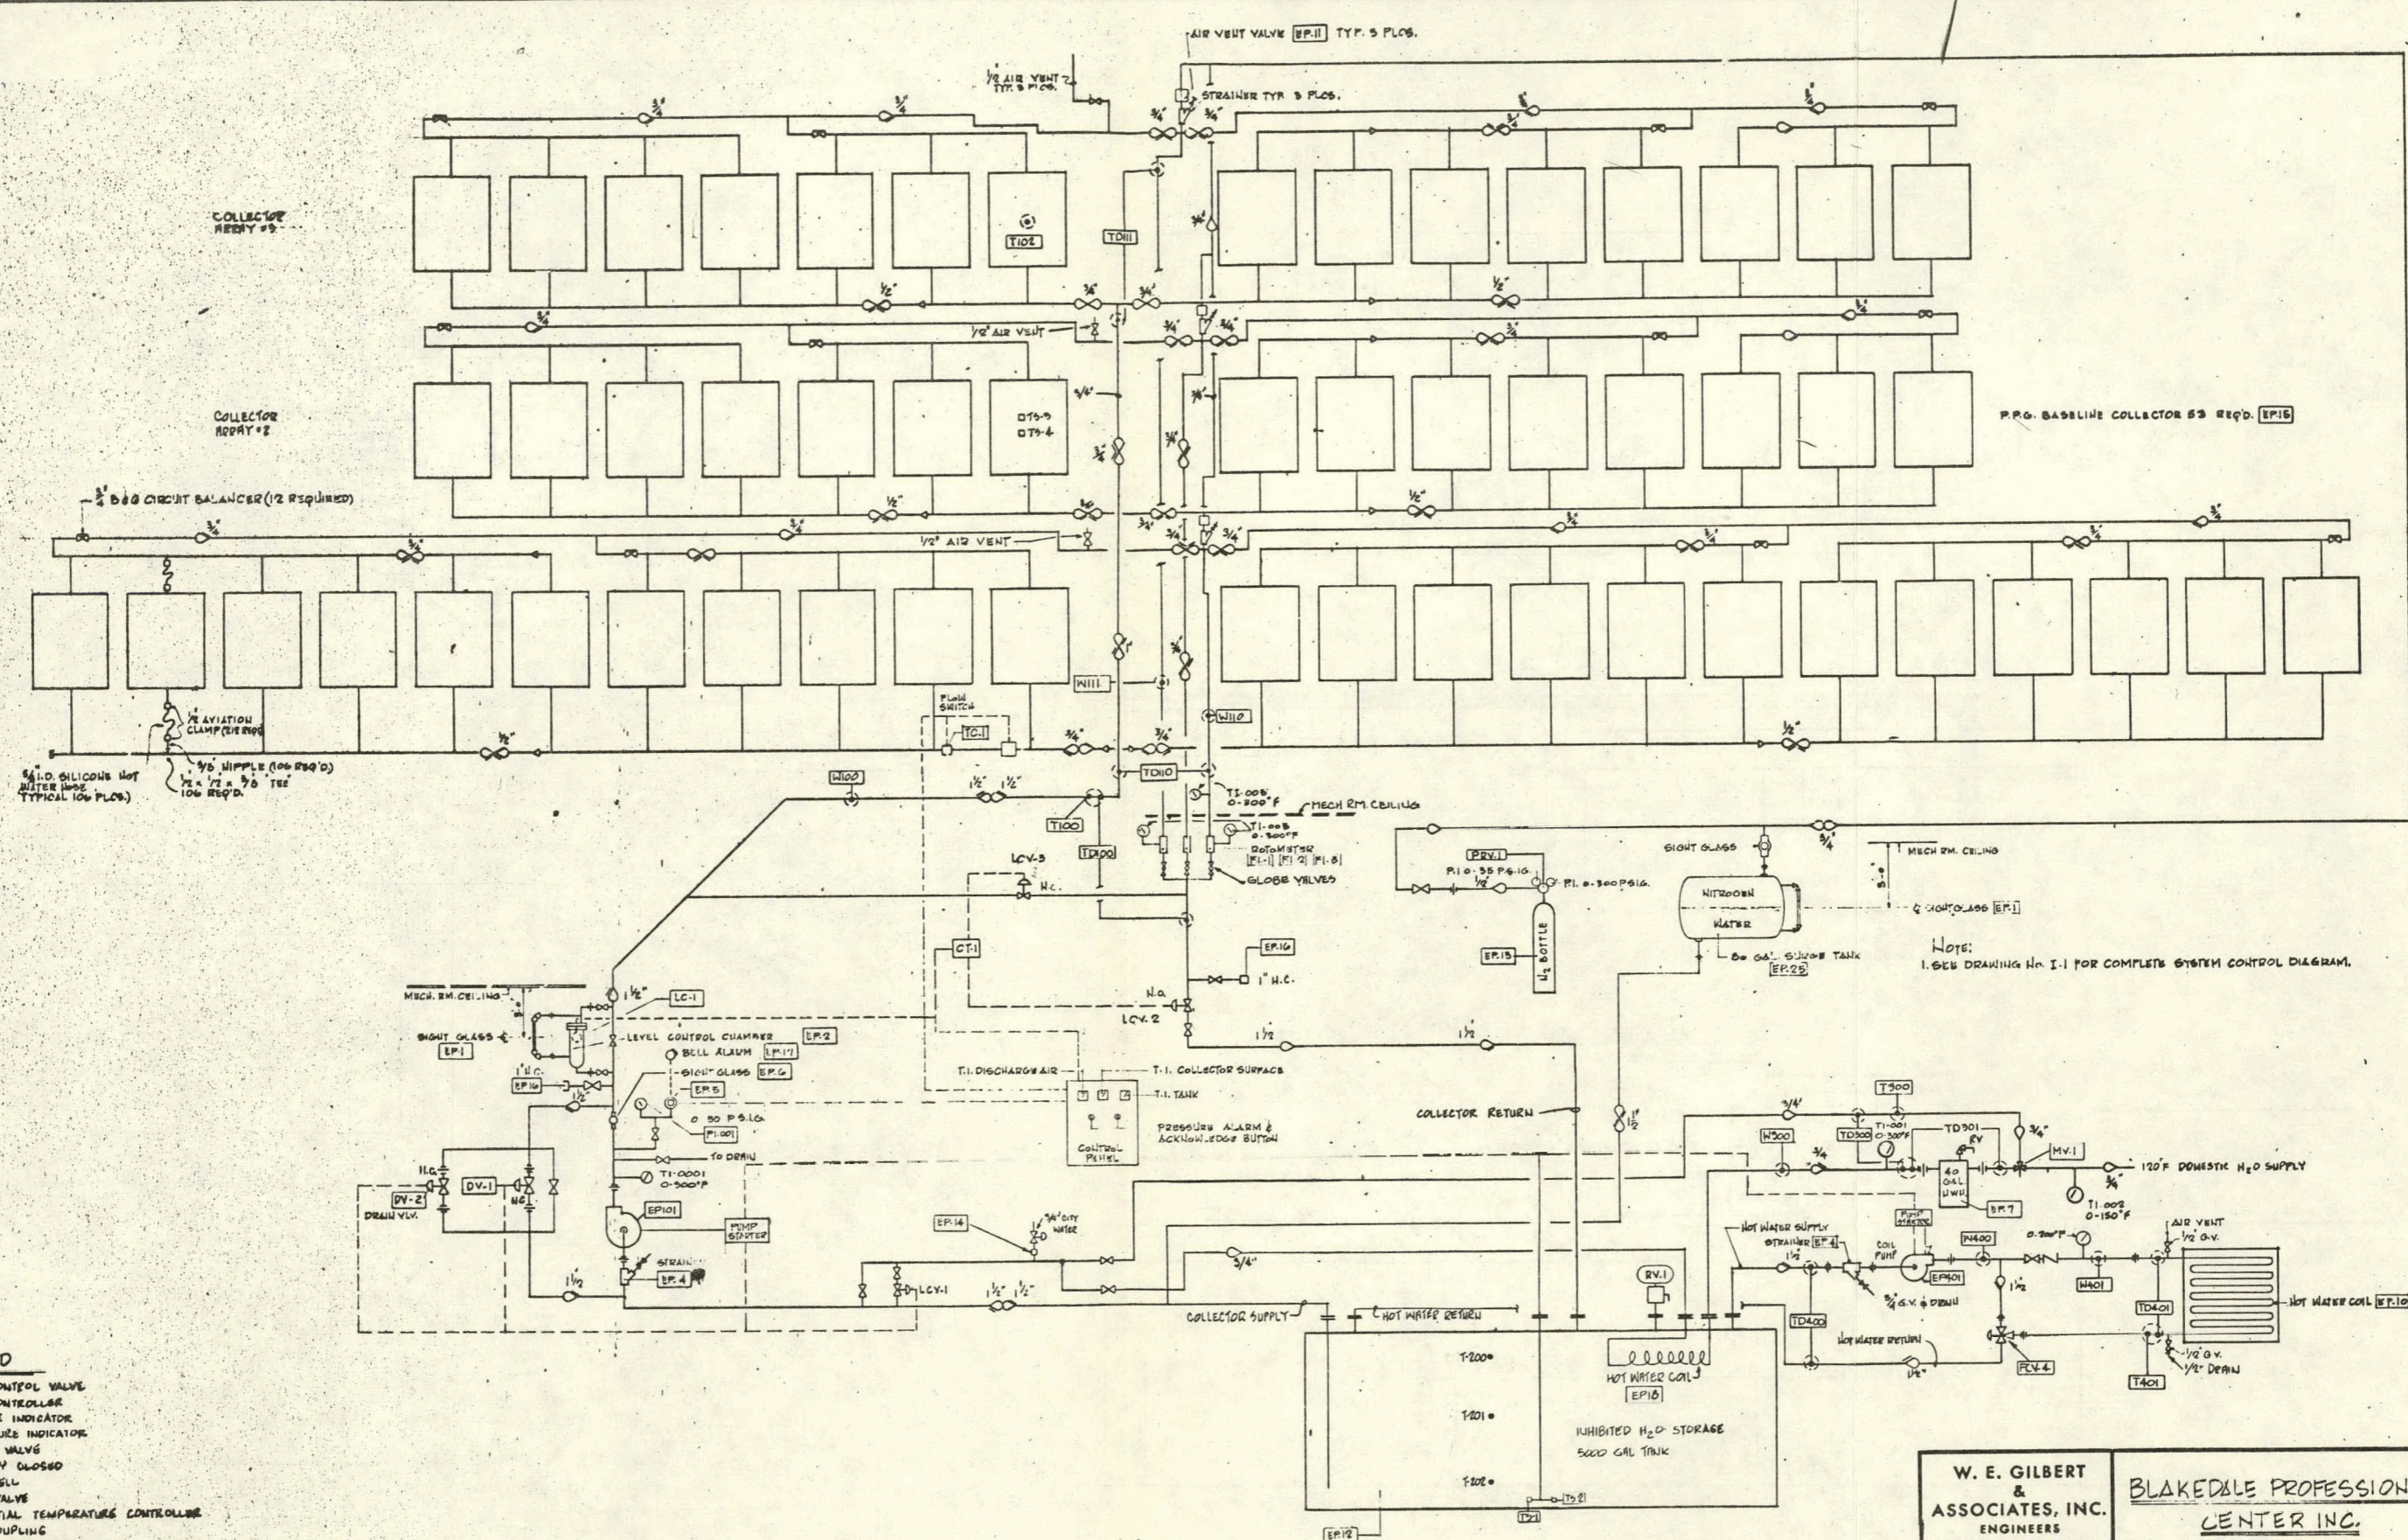


PRG. BASELINE COLLECTOR 53 REQ'D. [EP18]

NOTE:
1. SEE DRAWING No. I-1 FOR COMPLETE SYSTEM CONTROL DIAGRAM.

LEGEND


- LCV LEVEL CONTROL VALVE
- LC LEVEL CONTROLLER
- PI PRESSURE INDICATOR
- TI TEMPERATURE INDICATOR
- CV CONTROL VALVE
- NC NORMALLY CLOSED
- TW THERMOWELL
- RV RELIEF VALVE
- DTC DIFFERENTIAL TEMPERATURE CONTROLLER
- HC HOSE COUPLING
- CB CIRCUIT BALANCER
- 1" TANK INSULATED PIPE
- HWS HOT WATER SUPPLY
- HWR HOT WATER RETURN
- HPA HIGH PRESSURE ALARM
- LPA LOW PRESSURE ALARM
- TS TEMPERATURE SENSOR
- TC TEMPERATURE CONTROLLER
- ER ELECTRONIC RELAY
- FI FLOW INDICATOR

W. E. GILBERT & ASSOCIATES, INC. ENGINEERS GREENWOOD SOUTH CAROLINA HILTON HEAD SOUTH CAROLINA		BLAKEDALE PROFESSIONAL CENTER INC. SUITE No. 3 SOLAR HEATED HOT WATER FLOW DIAGRAM
DESIGNED A.L.S.	DATE MAR. 75	SHEET
DRAWN M.L.H.S.	SCALE 1/4" = 1'	P-1
CHECKED A.L.S.	FILE NO. 567	

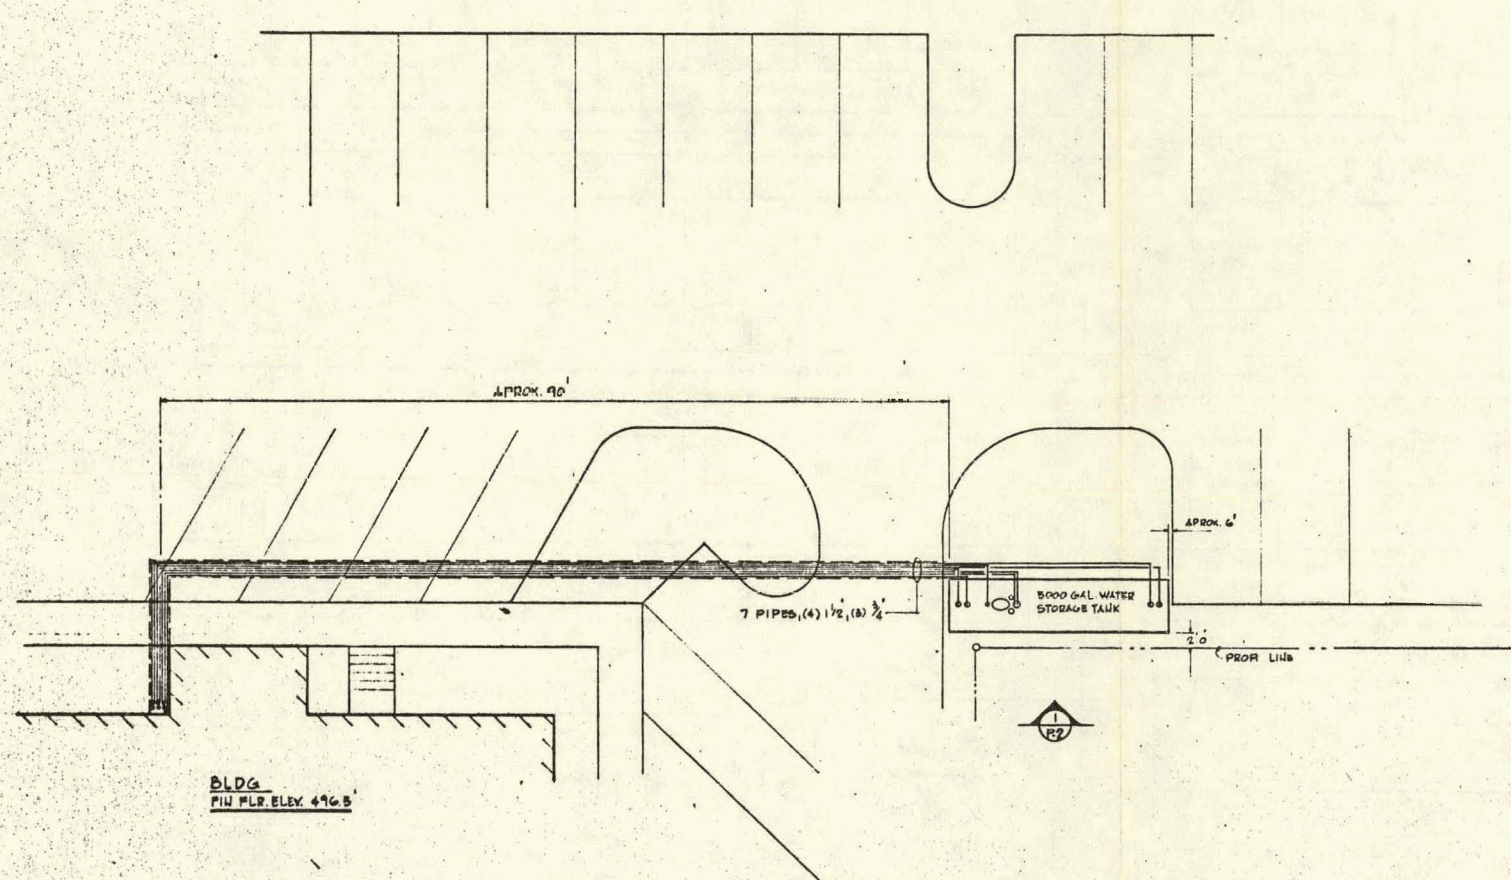


BLDG.
FIN. FLD. ELEV. 496.5


PARTIAL SITE PLAN
SCALE 10'-1"

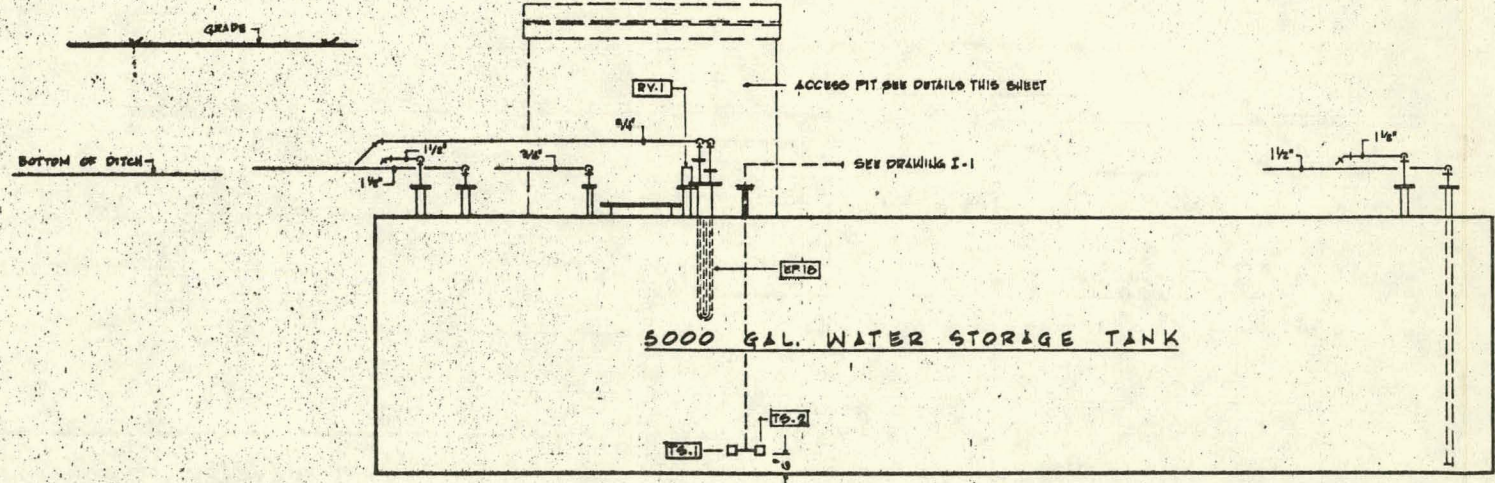

ELEVATION (1)
P.2

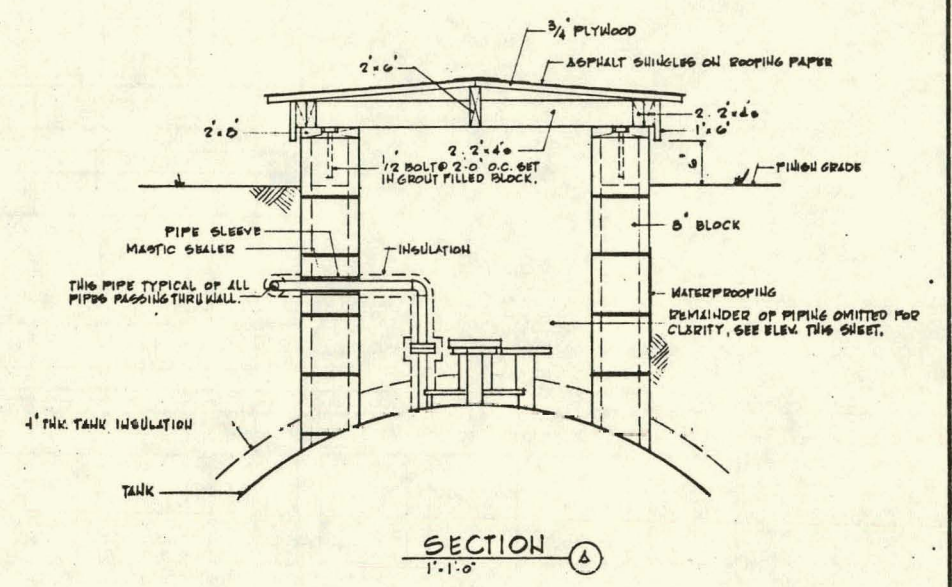


SECTION A
1'-1'-0"

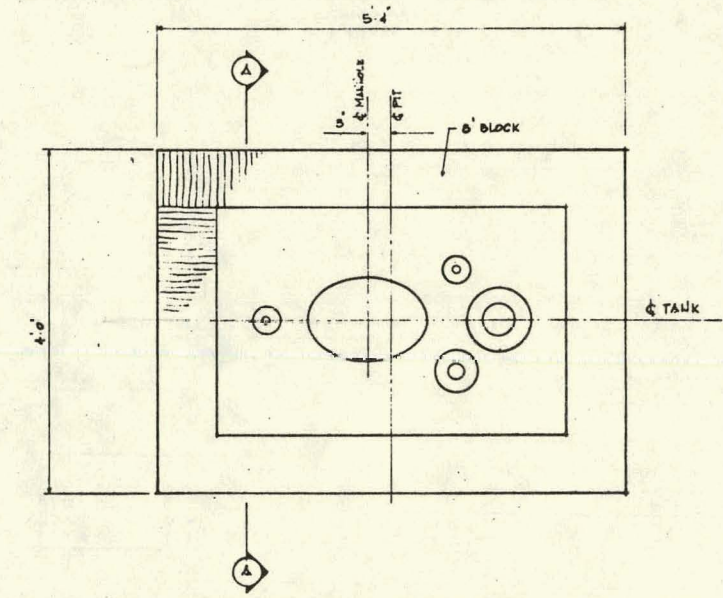

PLAN STORAGE TANK ACCESS PIT
1'-1'-0"




W. E. GILBERT
&
ASSOCIATES, INC.
ENGINEERS
GREENWOOD SOUTH CAROLINA HILTON HEAD SOUTH CAROLINA



BLAKEDALE PROFESSIONAL
CENTER, INC.
SUITE No. 3


OUTSIDE PIPING PLAN

DESIGNED A.L.G.	DATE Nov. 75	SHEET
DRAWN M.J.L.	SCALE AS SHOWN	P. 2
CHECKED A.L.G.	FILE NO. 569	

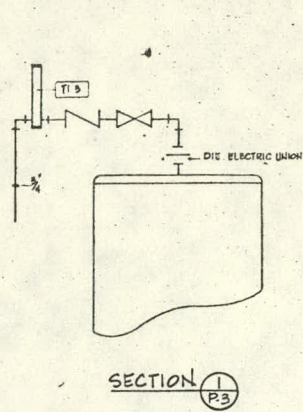


EP-20	BRNOX MODEL 120 AEROVANE TRANSMITTER W/MOUL-2417755-G-22 5-ON-1 ADAPTER
EP-21	EMPLY MODEL PSP SPECTRAL TRANSMITTER W/ACRYLIC TROUSER
EP-22	GENERAL ELECTRIC INSTRUMENTATION SUB-SYSTEM
EP-23	AIR HANDLER, GREEN 408012
EP-24	DUCT HEATER, 82 KW CARRIER

EQUIPMENT LIST	
DESIGNATION	DESCRIPTION
EP-1	LEVEL GAUGE - ERNST FIG. 55A 18" x 18" x 1/2" VLV.
EP-2	LEVEL CONTROL CHAMBER, AS PER DRAWING No. MS-1
EP-3	PUMP, TACO No. 1015 1/2" LINE PUMP, 1/2 HP, 200V/54/60HZ, 20 G.P.M. @ 30' HD.
EP-4	STRAINER - MUELLER #11, 50' HD. W/50 MESH 95 STRAINER.
EP-5	PRESSURE SWITCH, MERCID # DA 31-80, RANGE 1-55 P.S.I.G.
EP-6	DIGHT GLASS - ERNST FIG. 102 (BRONZE)
EP-7	WATER HEATER, "JACKSON" MOD. No. LJ-040-25, 40 GALL. STORAGE, 4.5 KW @ 240V.
EP-8	CONTROL PANEL, BIRBAER COLMAN
EP-9	PUMP, TACO No. 1015 1/2" LINE PUMP, 1/2 HP, 200V/54/60HZ, 20 G.P.M. @ 30' HD.
EP-10	COIL CARRIER MOD. No. 70-00U
EP-11	YELF VALVE, #70 WRIGHT-AUSTIN FLOAT TYPE
EP-12	STORAGE TANK, 6000 GAL. PER DWG. MS-2
EP-13	NITROGEN BOTTLE
EP-14	BACKFLOW PREVENTER, RAITS # 700
EP-15	COLLECTOR, 10 FT PITTSBURGH PLATE GLASS CO. "BASELINE"
EP-16	HOSE COUPLING, OFN # 93C
EP-17	BELL ALARM, EDWARDS # 874
EP-18	HEAT EXCHANGER, TACO # 4204-TA
EP-19	GENERAL ELECTRIC THERMAL ENERGY METER AND SOLAR ENERGY METER

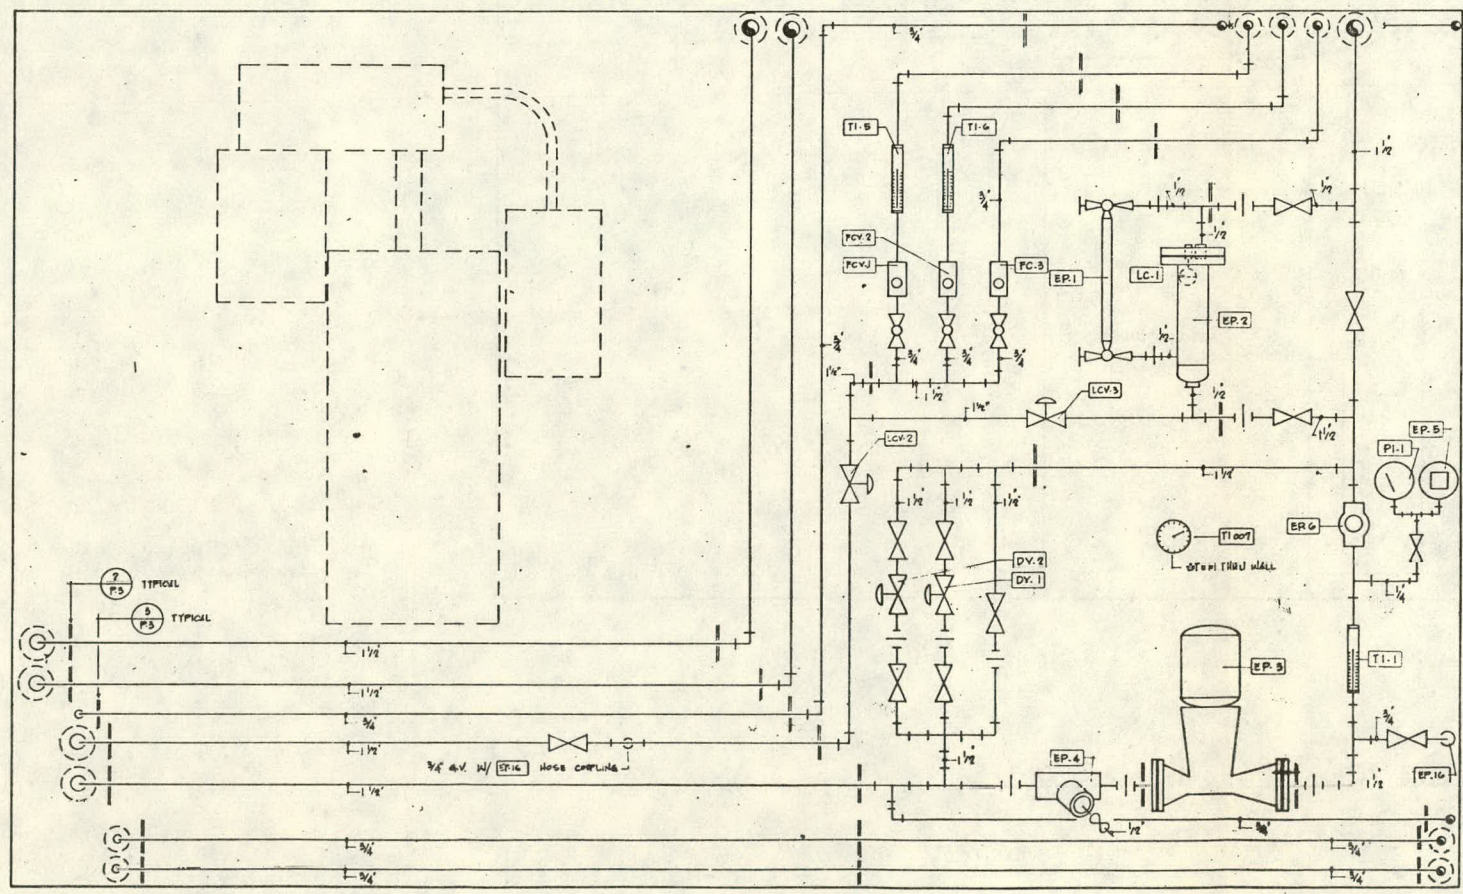


SOUTH WALL ELEVATION MECHANICAL ROOM
SOLAR PIPING PLAN
1 1/2 - 1 - 0

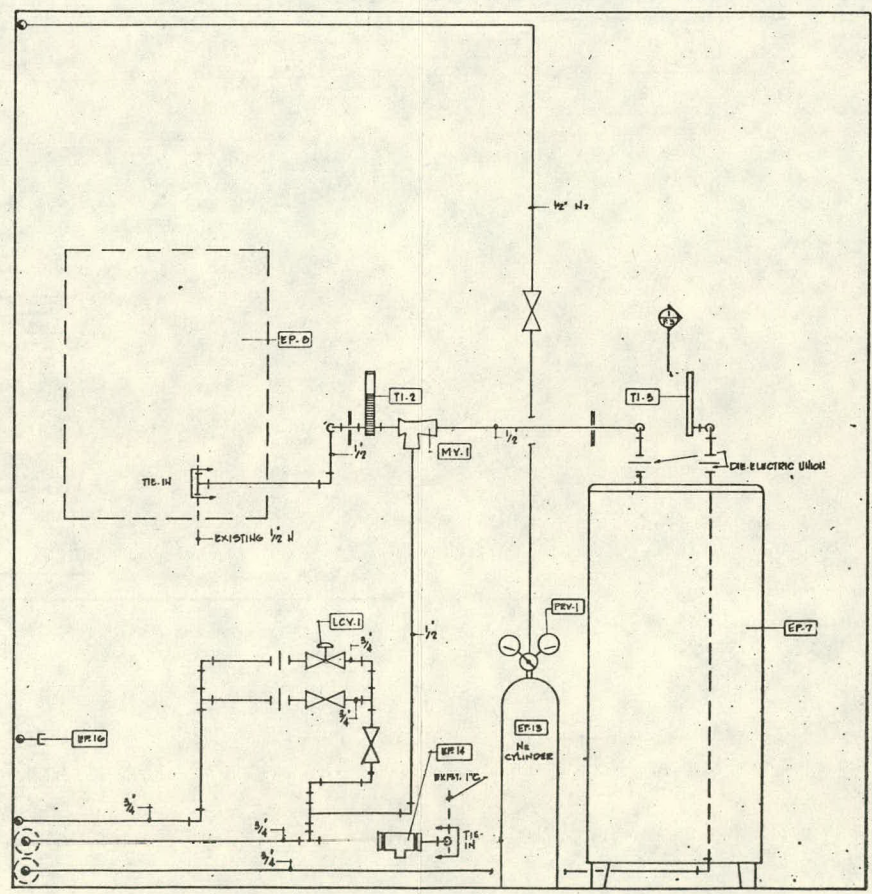

WEST WALL ELEVATION MECHANICAL ROOM
SOLAR PIPING PLAN
1 1/2 - 1 - 0


DESIGN RAN 8-17-79. *SEE GENERAL FOR REVISIONS

W. E. GILBERT & ASSOCIATES, INC. ENGINEERS		BLAKEDALE PROFESSIONAL CENTER, INC. SUITE No. 3	
SOUTH CAROLINA SOUTH CAROLINA			
SOLAR PIPING PLAN			
DESIGNED BY: J.M.L.	DATE: Nov. 78	SHEET	
DRAWN BY: J.M.L.	SCALE: AS SHOWN	P.3	
CHECKED BY: A.L.G.	FILE NO. 569		

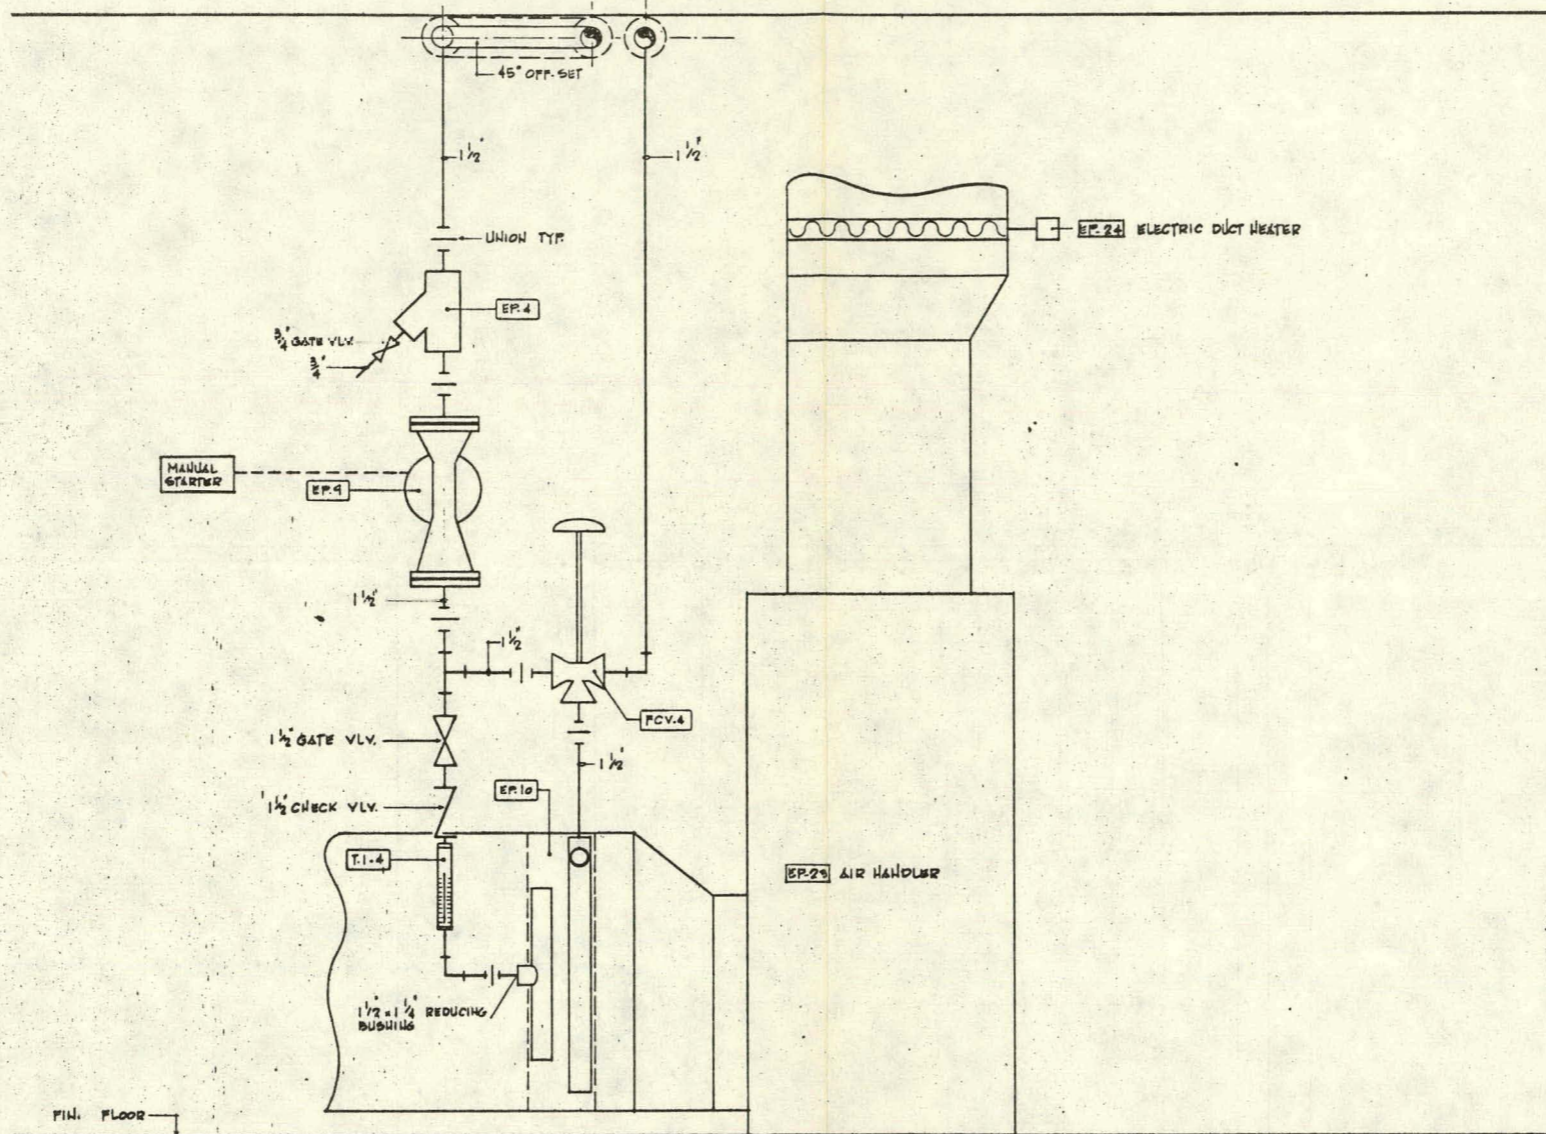


NORTH WALL ELEVATION MECHANICAL ROOM
 SOLAR PIPING PLAN
 1/2" = 1'-0"


W. E. GILBERT & ASSOCIATES, INC. ENGINEERS <small>GREENWOOD SOUTH CAROLINA HITCH HEAD SOUTH CAROLINA</small>		BLAKEDALE PROFESSIONAL CENTER, INC. SUITE No. 3 SOLAR PIPING PLAN	
DESIGNED BY: HOFFORD	DATE: NOV, 75	SHEET	
DRAWN BY: J.M.L.	SCALE: 1/2" = 1'-0"	P.4	
CHECKED BY: A.L.S.	FILE NO. 301		

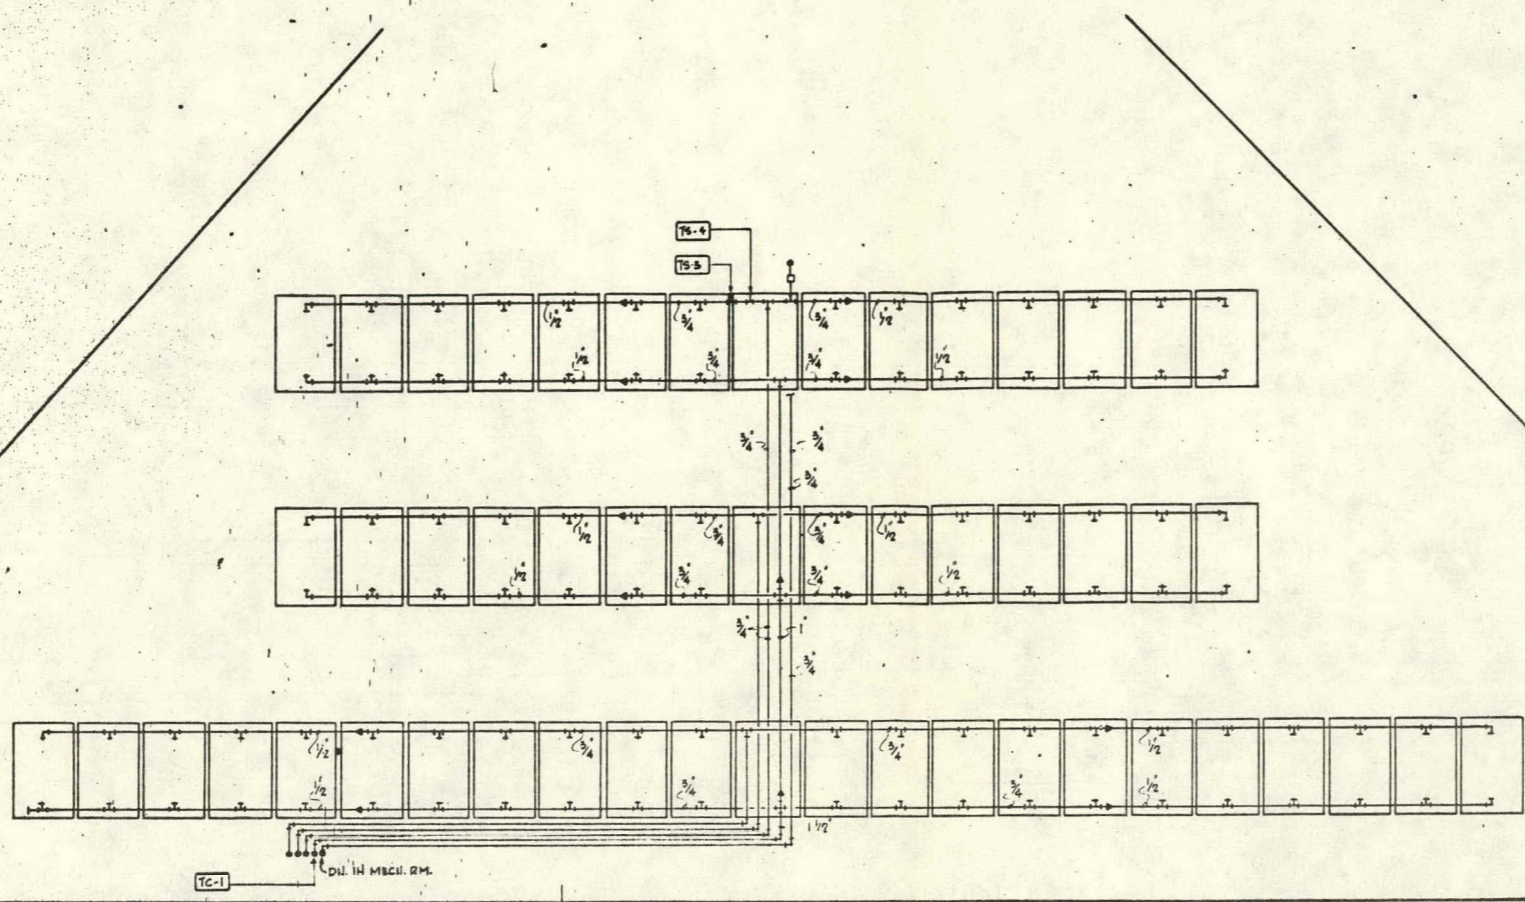


PLAN
SCALE 1/4" EQ. 1'-0"

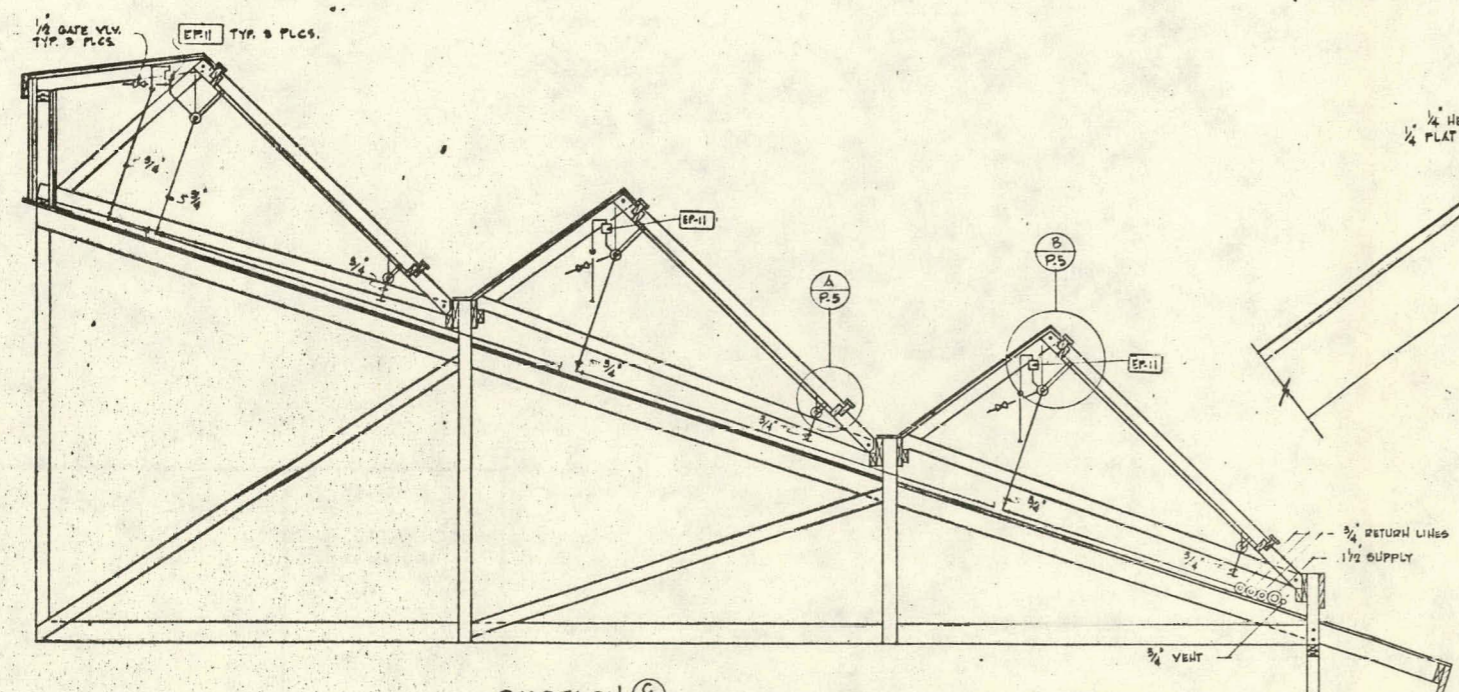

SECTION C
SCALE 1/2" EQ. 1'-0"

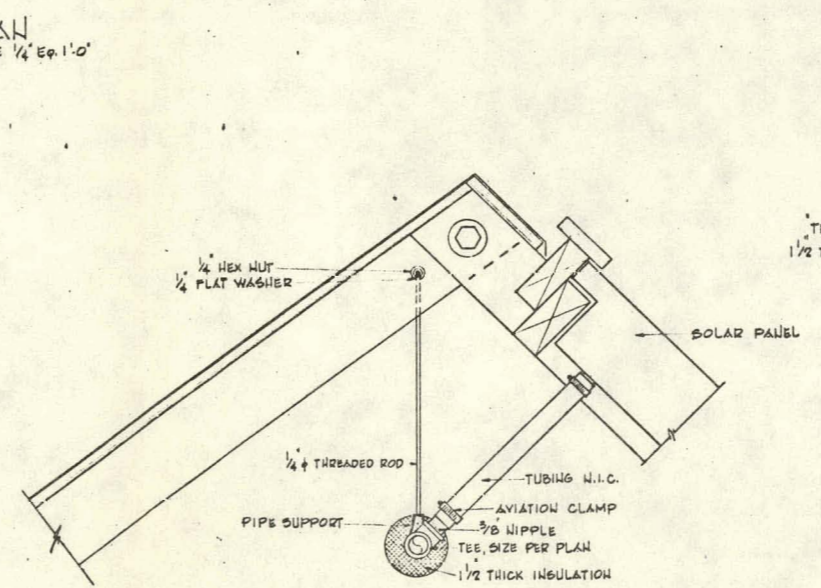

DETAIL A
SCALE 3" EQ. 1'-0"

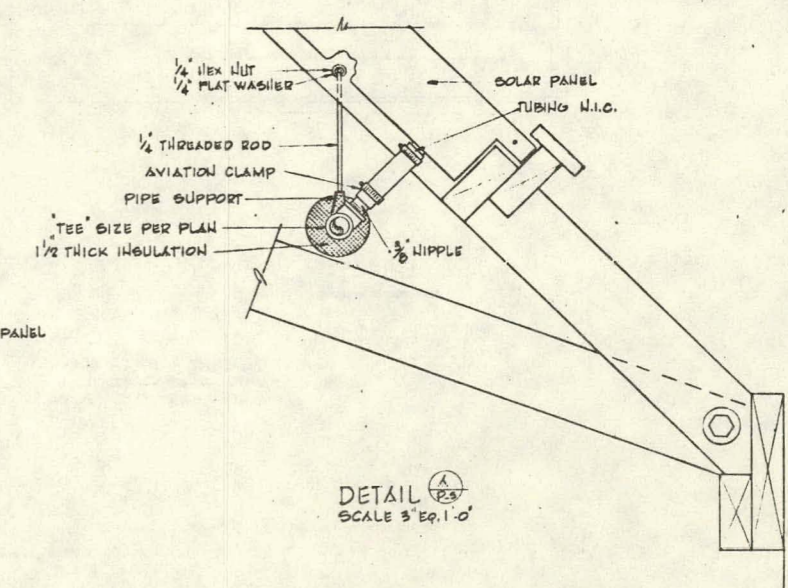


DETAIL B
SCALE 3" EQ. 1'-0"

W. E. GILBERT & ASSOCIATES, INC. ENGINEERS
GREENWOOD SOUTH CAROLINA HILTON HEAD SOUTH CAROLINA

BLAKEDALE PROFESSIONAL CENTER, INC.
SUITE No. 3


SOLAR PIPING PLAN

DESIGNED A.L.S.	DATE Nov. 75	SHEET
DRAWN R.J.L.	SCALE AS SHOWN	P.5
CHECKED A.L.S.	FILE NO. 569	

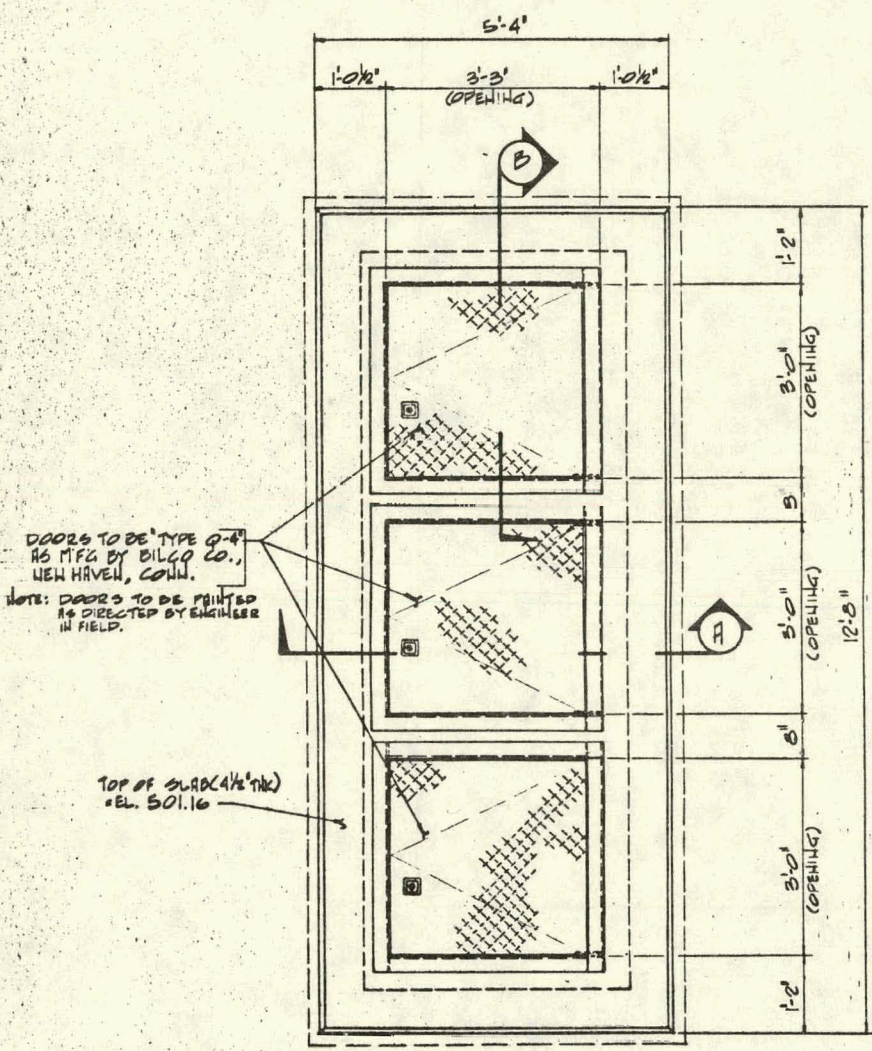

PLAN


NOTE: EL. 500' ASSUMED ELEV.
ON COR. OF SIDEWALK
& BACK COR. OF MAIN BLDG.

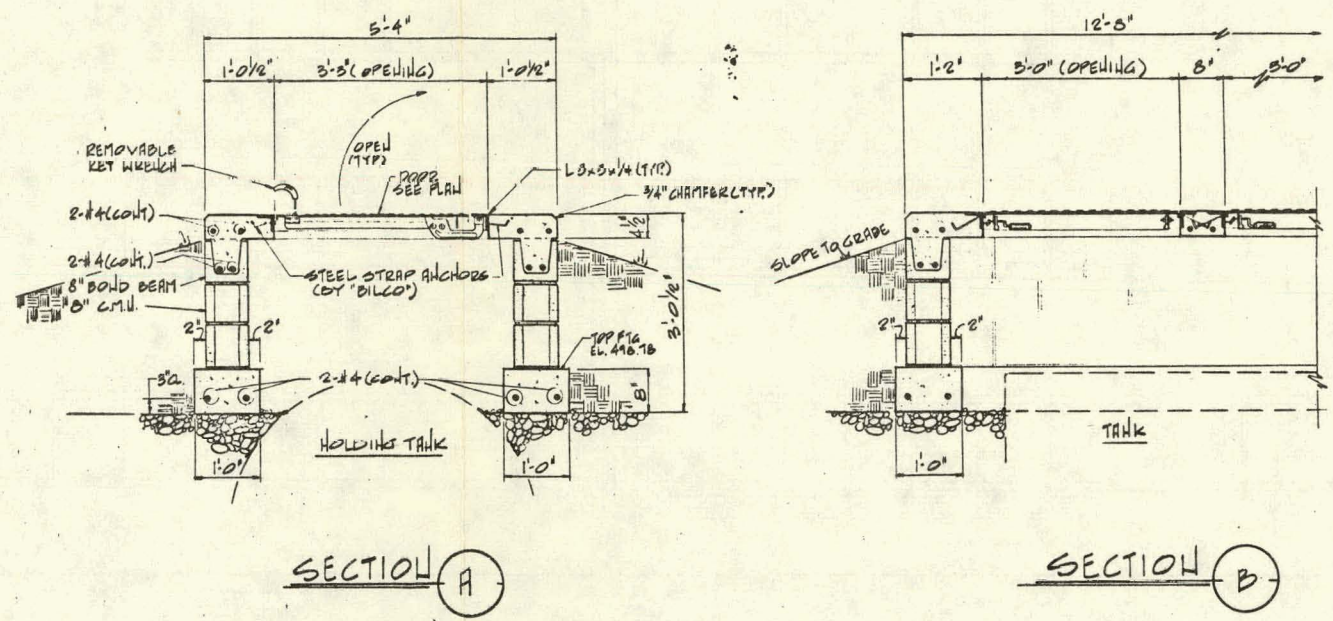

SECTION A


SECTION B

W. E. GILBERT & ASSOCIATES, INC. ENGINEERS <small>GREENWOOD SOUTH CAROLINA HILTON HEAD SOUTH CAROLINA</small>		TALK HOUSE
DESIGNED P.W.	DATE 5/17/77	SHEET
DRAWN M.R.E.	SCALE: 3/4" = 1'-0"	1 of 1
CHECKED P.W.	FILE NO. 569.01	


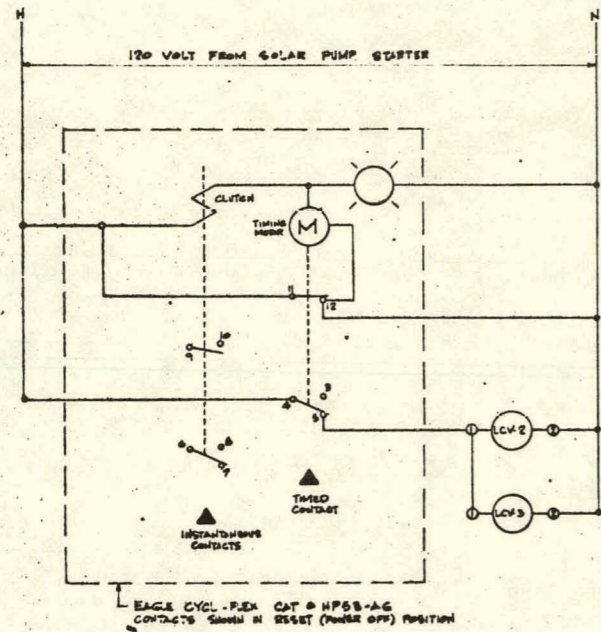


SEQUENCE OF OPERATION

1. 120 VOLT APPLIED WHEN SOLAR PUMP STARTS
2. TIMER CLUTCH ENERGIZED
 - (A) CONTACTS 7-10 & 6-8 CLOSE, 6-7 OPENS
 - (B) CONTACT 4-5 REMAINS CLOSED
 - (C) TIMING MOTOR STARTS
 - (D) LAMP & HORN ENERGIZED
3. TIMER TIMES OUT
 - (A) CONTACT 4-5 OPENS, DEENERGIZES LAMP & HORN
4. SOLAR PUMP STOPS, REMOVES 120 VOLT & TIMER RESETS

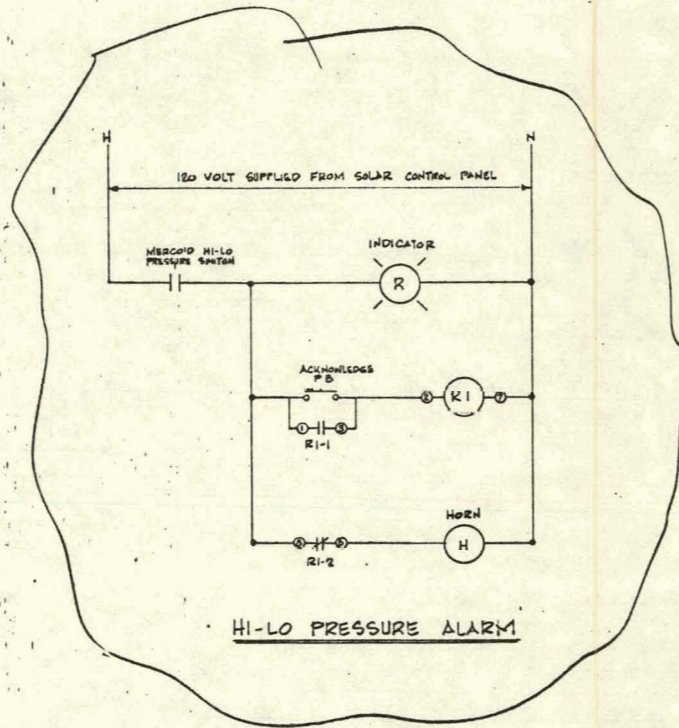


W. E. GILBERT & ASSOCIATES, INC. ENGINEERS GREENWOOD SOUTH CAROLINA WILTON HEAD SOUTH CAROLINA		
DESIGNED	DATE	SHEET
DRAWN	SCALE	
CHECKED	FILE NO.	


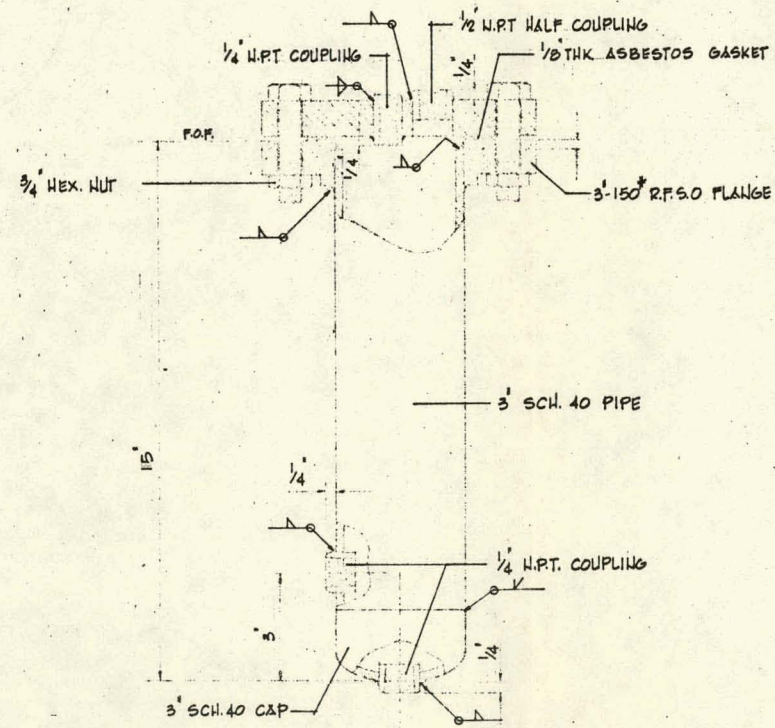
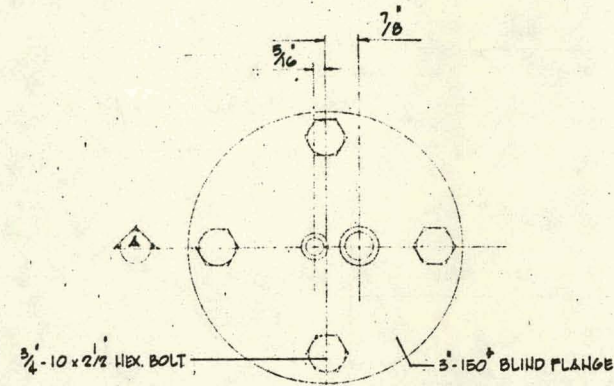


PARTIAL SECTION A
SCALE 3/8" EQ 1"

Note:
ALL MATERIALS TO BE CARBON STEEL.

W. E. GILBERT & ASSOCIATES, INC. ENGINEERS <small>COLUMBIA, SOUTH CAROLINA COLUMBIA, SOUTH CAROLINA</small>		BLAKEDALE PROFESSIONAL CENTER, INC. SUITE No. 3	
LEVEL CONTROL CHAMBER			
DESIGNED	ALS	DATE	NOV. 78
DRAWN	M.L.	SCALE	AS SHOWN
CHECKED	ALS	FIG. NO.	309



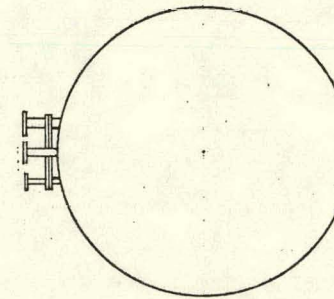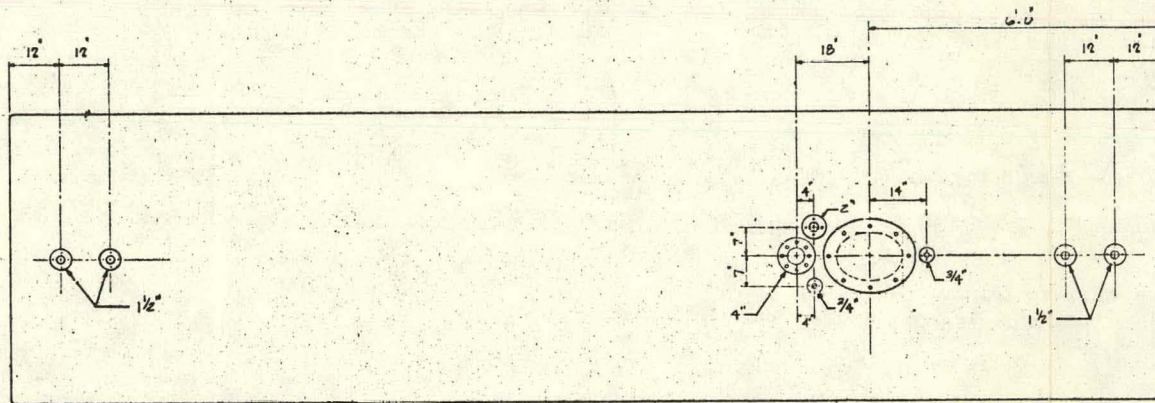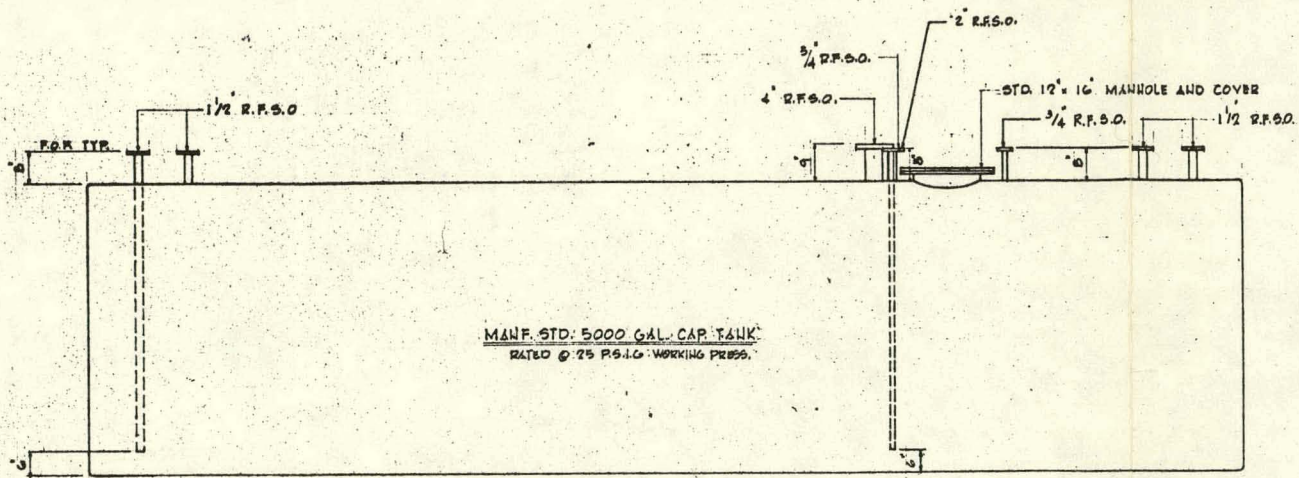

NOTE:
 ALL FLANGES INDICATED ON DWG. ARE TO BE 150 LB. RAISED FACE
 SLIP ON.
 ALL PIPING INDICATED ON DWG. IS TO BE SCH. 40 A-53
 SEAMLESS.

HOT WATER STORAGE TANK
 1/2 eq1-0'

W. E. GILBERT & ASSOCIATES, INC. ENGINEERS <small>DEPT. OF ENGINEERING SOUTH CAROLINA STATE UNIVERSITY COLUMBIA, SOUTH CAROLINA</small>	BLAKEDALE PROFESSIONAL CENTER, INC. SUITE No. 3	
	HOT WATER STORAGE TANK	
	DRAWN A.L.S. CHECKED M.J.L. DATE Nov. 75 SCALE 1/8" = 1'-0"	MS-2
